

MEE EVENTS

Current State, Pending Work & Master Build Roadmap

Customer + Vendor + Worker Mobile | Employee Mobile | CRM | ERP | Backend | Database | Release

Document	Value
Version	1.0
Document date	18 August 2026
Repository audit date	18 August 2026
Repository	Mee Event V1
Audit basis	Source code, configuration, SQL migrations, tests, build output, Git state, and current documentation
Product decision	Continue the existing repository; do not restart

Founder summary: There is one Flutter application today, not two duplicate apps. It serves Customer, Vendor, and Worker roles. The required Employee Mobile application does not exist as a production application yet. Continue this repository, stabilize it first, and add Employee Mobile later as a separate Flutter application connected to the same NestJS backend and PostgreSQL database.

1. Executive Summary

Where am I now?

Mee Events is a substantial connected-platform foundation, not a finished production product and not a project that should be restarted. The repository already contains:

- one Flutter Customer/Vendor/Worker application;
- one NestJS modular backend with 17 routed feature modules and about 223 controller handlers;
- one Next.js employee portal with CRM and ERP routes;
- 20 ordered PostgreSQL migrations creating 114 tables;
- shared roles, capabilities, schemas, audit and outbox foundations;
- a connected demo path from customer enquiry to CRM, quotation, advance confirmation, booking and Event Record.

The project is strongest in backend and database foundations. It is weakest in production proof, complete role products, employee work management, integrations, automated end-to-end testing, release configuration, and deployment.


Direct answers

Question	Evidence-based answer
Start new or continue?	Continue this repository. Restarting would discard valuable connected backend, database and UI work.
Are there two Flutter apps?	No. Only <code>apps/mobile</code> is a Flutter package.
Are there duplicate Customer/Vendor/Worker apps?	No. Customer, Vendor and Worker are role experiences in one app.
Does Employee Mobile exist?	No production app. Some manager/operations Flutter screens exist inside <code>apps/mobile</code> , but the login/bootstrap sends employee roles to <code>employee_web</code> ; those screens are reusable code, not an Employee Mobile product.
Should useless files be permanently deleted now?	No bulk deletion. First make a reviewed cleanup list. Regenerable build/cache folders and proven junk are safe candidates; uncertain design/evidence files must be archived or reviewed.
Is the project production-ready?	No. Production OTP, payment gateway, document storage/PDF, notifications, database integration tests, E2E, monitoring/deployment, signing and store release proof are incomplete.
What should be done now?	Module STAB-01: restore the repository quality gate. Fix current formatter/lint/mobile test failures, separate raw design exports from source formatting, and prove the full local verification command is green.

Current completion view

Class	Current state
Completed	Monorepo architecture; NestJS/PostgreSQL direction; Flutter framework decision; shared contracts; backend auth/session foundation; server capability checks; branch context; audit/outbox foundations; broad backend module foundations; TypeScript tests/build/typecheck; Flutter analyzer; two deprecated Flutter API fixes already removed analyzer errors.
Partial	Customer app; Vendor ops; Worker ops; CRM leads/quotes; ERP event/vendor/worker/inventory/finance/operations; payment recording; notification intent; CI; documentation.
Broken	Root format gate; root lint gate; 20 Flutter Home widget tests; production Android release signing; production OTP delivery; invalid image assets; CI branch/API-port drift.
Missing	Separate Employee Mobile app; generic employee work management; production file storage; real quotation PDF; payment gateway/webhooks; notification delivery; full vendor/worker products; procurement; employee hierarchy/targets/campaigns; database integration and E2E suites; production hosting/CD/store pipelines.
Blocking	Docker is unavailable for database proof; business/provider choices for OTP, payments, files, hosting and social channels are open; employee role/work-item architecture needs an ADR.
Next	Make all existing gates green before adding modules.

Recommended product shape




One backend and one database remain authoritative. The two mobile applications are separate store products because they serve different audiences and release concerns; they do not duplicate business logic or data.

2. Current Architecture

Actual repository layout

Location	Technology	Actual responsibility	Status
apps/mobile	Flutter	One application: Customer plus Vendor/Worker operations through AppGateway	PARTIAL
apps/backend	NestJS	Versioned API, identity, authorization and business modules	IMPLEMENTED — UNVERIFIED against real Postgres
apps/erp-web	Next.js	One employee web portal containing CRM and ERP routes	PARTIAL
packages/api-contracts	TypeScript/Zod	Shared wire schemas, statuses and request/response contracts	DONE foundation
packages/shared-types	TypeScript	Shared platform roles/session types	DONE foundation
infrastructure/postgres/migrations	SQL	Ordered PostgreSQL source-of-truth schema	IMPLEMENTED — UNVERIFIED in this audit
infrastructure/docker-compose.yml	Docker Compose	Local PostgreSQL and Redis only	BLOCKED locally because Docker daemon is unavailable
.github/workflows/ci.yml	GitHub Actions	TypeScript and Flutter checks, debug APK only	PARTIAL / MISCONFIGURED

Actual request/data path

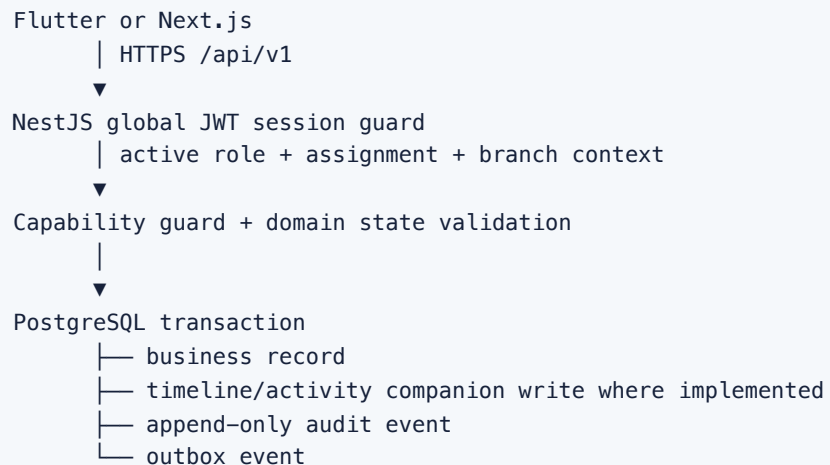

The accepted architecture says all controlled writes go through NestJS. A direct Supabase client remains initialized and bundled in the Flutter app, creating architecture and secret-surface risk even if its current data path is mostly dormant.

Current client surfaces

The backend and shared contract expose only `customer_mobile`, `vendor_mobile`, `worker_mobile`, and `employee_web`. Employee, support, finance, manager, administrator and auditor roles currently resolve to `employee_web`. There is no `employee_mobile` client surface.

3. Current Repository Audit

Repository facts at audit time

Measure	Finding
Git branch	<code>master</code> , two commits ahead of <code>origin/master</code>
Working tree	145 modified/added tracked files, 26 tracked deletions, 102 untracked files
Flutter applications	1 (<code>apps/mobile</code>)
Dart files under mobile <code>lib</code>	172
Mobile test files	26
Backend source TypeScript files	129
Backend spec files	30
ERP <code>page.tsx</code> files	44
Built ERP routes	37
SQL migrations	20 (<code>0001</code> – <code>0020</code>)
PostgreSQL tables declared	114
Routed backend feature modules	17
Controller handlers counted	about 223

Mobile audit

- Package: `mee_events` , version `1.0.0+1` .
- Customer navigation is currently **Home, Explore, Plan, Enquiries, Account**. The approved target in this roadmap is **Home, Explore, Enquire, Plan, Profile**. This is Open Decision OD-01 because routes, tests and mental models must be migrated intentionally.
- Customer has Home, Explore, Plan, enquiry/checkout/detail/success, quotation, event workspace, account/profile, favorites, search and catalogue screens. Home/Explore still contain sample/fallback content and placeholder actions.
- Vendor has a live operations dashboard, assignments and progress. It is not yet the full vendor product.
- Worker has a dashboard and task detail/progress/attendance foundations. It is not yet the full worker product.

- Manager, operations, inventory and finance-oriented Flutter screens are present but not reachable from the production gateway for employee roles. Treat as reuse candidates after architecture review, not a second app.
- Placeholder gaps found: quotation PDF unavailable, booking confirmation PDF unavailable, feedback “coming soon”, notification action disabled, map/location placeholder and incomplete subcategory navigation.
- Flutter `.env` is bundled as an asset; Supabase is initialized directly and `SupabaseService` reads `event_services`. This conflicts with the backend-only data boundary.

Backend audit

Feature areas are identity, platform, catalogue, search, enquiries, CRM, quotations, payments, bookings, Event Records, manager operations, vendors, workers, inventory, finance and operations, plus health and audit support.

Security foundations found:

- OTP request/verify flow with 300-second TTL, 60-second resend cooldown, five verification attempts and five requests per hour;
- 15-minute JWT access token and rotating opaque refresh token;
- 30-day revocable device session and refresh-reuse revocation;
- active-role and active-assignment checks;
- server capability guard and branch/resource context;
- production refuses local OTP;
- request identifiers, audit trail and sensitive-log redaction.

Production gaps found:

- the external OTP provider path returns a 503 placeholder and its endpoint/key are not in validated environment schema;
- `idempotency_records` exists, but no application use or `Idempotency-Key` handling was found;
- quotation documents store a `pdf_placeholder`; there is no real protected PDF pipeline;
- file/photo APIs largely store a client-supplied storage key; object storage, upload validation and signed access are missing;
- payment is an operator-confirmed reference flow, not a real gateway/webhook/reconciliation implementation;
- notifications are mostly outbox intent with `pushIntegrated: false`; only narrow processors exist;
- Redis is provisioned locally but not used by backend code;
- no generic employee work-item/assignment model, employee hierarchy, department, target or campaign model was found.

CRM/ERP web audit

Live routes exist for leads, quotations, bookings, Event Records, manager tasks, vendors, workers, inventory, warehouse, operations and finance. `employee-api.ts` provides a broad live API client. Login uses OTP, access token and refresh handling.

Important limits:

- the root dashboard uses illustrative metrics and reports the central backend as not connected, even though feature pages use live APIs;

- route protection is mainly client-side session checks; no global Next middleware/server authorization layer was found;
- CRM lacks a complete My Work, normalized follow-up queue, Customer 360, pipeline management, team workload, targets and reports product;
- ERP lacks complete procurement, administration, approval inbox and reporting products;
- `dummy-leads.ts` appears to be a legacy/sample candidate and must be proven unreachable before deletion;
- only two ERP Vitest specs exist; there is no browser E2E suite.

Database audit

The 114 tables cover identity/session/roles, branch, catalogue, enquiries/leads, quotations/payments/bookings, Event Records, manager tasks, vendors, workers, inventory/warehouse, operations, finance, timelines, activities, audit and outbox.

Not found as complete product domains: vendor applications and full listing/version/pricing workflow, worker applications/availability workflow, generic employee/work items/hierarchy, procurement purchase orders/goods receipts, in-app notification centre, customer reviews, campaigns/targets, and complete admin/reporting models.

Quality-gate evidence on 18 August 2026

Gate	Result	Evidence
TypeScript formatting	BROKEN	280 findings; raw Stitch exports include invalid/gzipped <code>.js</code> files
TypeScript lint	BROKEN	one Next.js <code></code> warning, with zero warnings allowed
TypeScript typecheck	PASS	workspace packages pass sequential typecheck
TypeScript tests	PASS	backend 30 files/173 tests; ERP 2 files/2 tests
TypeScript build	PASS WITH WARNING	packages/backend/ERP build; Next produces 37 routes and the image warning
Flutter analyze	PASS	zero issues with <code>--fatal-infos</code> ; the two deprecated API errors have been fixed
Flutter tests	BROKEN	415 passed, 20 failed, all in <code>home_tab_test.dart</code>
PostgreSQL integration	BLOCKED / MISSING	Docker daemon unavailable; CI has no database service
Browser/device E2E	MISSING	no Playwright, Cypress, Detox or equivalent suite

Duplicate, unwanted and cleanup audit

Proven regenerable cleanup candidates

Path/group	Approximate size	Action
apps/mobile/build	4.05 GiB	Safe to regenerate; delete only in a dedicated reviewed cleanup
apps/mobile/.dart_tool	1.09 GiB	Safe to regenerate
root node_modules	560 MiB	Safe to reinstall
root .pnpm-store	510 MiB	Safe to recreate
apps/erp-web/.next	124 MiB	Safe to rebuild
apps/mobile/android/.gradle	14 MiB	Safe to regenerate
apps/backend/dist	3 MiB	Safe to rebuild

Together these consume about 6.3 GiB. They are not duplicate applications.

Proven junk or broken assets

- .DS_Store files in repository folders;
- local debug logs such as .cursor/debug*.log , design/pw-out.log , and apps/mobile/flutter_web.log ;
- 24 image files that are only 29-byte HTML 404 responses, including home/banners/concert.jpg and multiple engagement/mehndi/pre-wedding/sangeet/wedding subcategory assets;
- 19 exact duplicate asset hash groups across mobile assets and design exports;
- literal duplicate erp_warehouse.read in the manager capability list;
- documentation drift: old test counts, “current phase engineering documentation”, outdated customer navigation, CI branch/port mismatch and a broken production-document ADR link.

Review before any deletion

- design/stitch-screens contains raw/debug exports and gzipped data misnamed as JavaScript. Exclude or archive it; do not format it as source and do not bulk-delete without confirming design value.
- artifacts contains evidence and media/licensing material. Move to an agreed archive outside Git if desired; do not destroy it.
- unreachable/sample code such as dummy-leads.ts and stranded manager/operations Flutter screens must be dependency-searched and reviewed before removal or extraction.

No product source or user evidence was deleted during this audit.

4. Completed Work

The following is complete at foundation level and supported by current source/test evidence:

1. Monorepo separation of mobile, backend, employee web, contracts, shared types and migrations.
2. Accepted Flutter + NestJS + Next.js + PostgreSQL architecture.
3. Shared platform role set and server capability map.
4. OTP challenge, token/session rotation/revocation and production-local-OTP rejection.
5. Backend request validation, authenticated principal, active-role/branch context and capability guard.
6. Enquiry creation and CRM lead creation in one transaction.
7. Quotation/advance/booking/Event Record foundation workflow.
8. Backend foundations for manager, vendor, worker, inventory, operations and finance.
9. Append-only audit and outbox patterns across many controlled mutations.
10. Ordered migrations through `0020` and a 114-table connected schema foundation.
11. TypeScript typecheck, backend/ERP unit tests and production builds pass.
12. Flutter analyzer is green; the two deprecated Flutter API errors are fixed.

“Completed foundation” does not mean store-ready or production-proven. Database integration, E2E and live providers remain required.

5. Partial Work

Area	What exists	What remains
Customer	Broad screen set and connected enquiry/quote/payment/event path	Correct navigation, live Home/Explore data, robust states, PDF, real payment, feedback and full tests
Vendor	Ops dashboard, assignment response/progress, backend registry/assignment/settlement foundations	Application/KYC, catalogue/listings/pricing/availability, earnings/profile/reviews and complete UX
Worker	Dashboard, task detail, response/progress/attendance, backend registry/task/payout foundations	Application/approval, skills/availability/profile/earnings/incidents/proof and complete UX
CRM	Lead list/detail, claim, requirements, quotations and conversion APIs	My Work, follow-up queue, Customer 360, pipeline, team, targets, reports and activity product
ERP	Event, manager, vendor, worker, inventory, warehouse, operations and finance routes/APIs	Procurement, approvals, admin, reports, real overview and full workflow verification
Notifications	Outbox topics and limited processors	Provider delivery, retries/dead-letter, preferences, inbox, push token lifecycle and escalation rules
Files/documents	Storage-key fields and PDF placeholders	Secure object storage, upload/download validation, signed URLs, malware/content controls and PDF generation
CI/CD	Formatting/lint/type/test/build jobs and debug Flutter APK	Correct branch/port, database integration, release builds, signing, staging deploy, CD and rollback

6. Broken / Risky Work

1. **Quality gate red:** root format/lint and 20 Flutter Home tests fail.
 2. **Android release signing:** release currently uses debug signing; production release must be blocked.
 3. **iOS release not established:** bundle/provisioning/team, flavors and TestFlight pipeline are unverified.
 4. **CI drift:** workflow runs pushes to `main` while active branch is `master`; Flutter points to API port 3000 while the backend uses 3002.
 5. **Direct Supabase client in Flutter:** violates backend-only data boundary and bundles `.env`.
 6. **Invalid image assets:** 24 files are HTML 404 payloads, not images.
 7. **Production OTP missing:** the external path intentionally fails.
 8. **Financial flow is not gateway-backed:** manual references can be useful for a controlled pilot but cannot be described as automated payment confirmation.
 9. **No real PDF/file security:** placeholders and client-provided keys cannot protect quotations, KYC or evidence.
 10. **No database integration/E2E proof:** passing unit tests use fakes and do not prove migrations or user journeys.
 11. **Sample dashboards/data can mislead:** customer catalogue fallbacks and ERP overview are not authoritative.
 12. **Dirty worktree:** hundreds of changes make cleanup/refactoring risky until changes are grouped and protected.
-

7. Pending Work

The main pending products are:

- complete Customer modules with the final navigation;
 - complete Vendor and Worker onboarding/self-service products;
 - employee work management and follow-up model;
 - separate Employee Mobile application built role by role;
 - full CRM workflow and management visibility;
 - procurement, approvals, administration and reports;
 - production OTP, files/PDF, payment and notification integrations;
 - real database/API/E2E/security/performance/recovery tests;
 - staging/production infrastructure, monitoring, backup proof and release automation;
 - both Flutter applications signed and released through Google Play and Apple App Store.
-

8. Blocking Issues

Blocker	Blocks	Resolution
Docker daemon unavailable	Real migration, repository and smoke proof	Start Docker; run clean DB migration plus connected smokes
Red quality gates	Safe feature development and CI confidence	Complete STAB-01
Employee role/work-item model not approved	Employee Mobile, My Work, SLA/escalation and management reporting	Decide OD-03/OD-04 and write ADR/migration plan
OTP provider not selected/wired	Production authentication	Select provider, data handling and failover; implement/test
Payment mode/provider undecided	Automated confirmation/refunds/reconciliation	Approve pilot versus gateway strategy
Object storage/provider undecided	PDF, KYC, proof and private documents	Approve storage, keys, access and retention
Social lead channels/consent undecided	CRM social integrations	Choose channels/providers and lawful consent/retention model
Hosting/monitoring ownership undecided	Staging and production	Approve platform, budget, regions, backup and incident owner
App identities/signing accounts incomplete	Store releases	Confirm final bundle IDs, organization accounts and signing custody

9. Product Architecture

Target applications

Product	Target implementation	Rule
Customer/Vendor/Worker Mobile	Continue <code>apps/mobile</code> Flutter	One public multi-role app; role/capability-driven experience
Employee Mobile	New <code>apps/employee-mobile</code> Flutter after ADR	Mobile-first work execution; not a miniature ERP; same backend/data
Employee Web	Continue <code>apps/erp-web</code> Next.js	CRM and ERP in one secure portal
Backend	Continue <code>apps/backend</code> NestJS	Only business/API layer; no second backend
Database	Continue PostgreSQL migrations	One source of truth; no per-app databases

Data consistency rule

Interfaces show projections of the same identifiers and records. They do not copy Customer, Enquiry, Lead, Quotation, Booking, Event Record, Vendor, Worker, Task or Finance records to create convenience silos. Changes travel through versioned NestJS commands and authoritative PostgreSQL transactions.

Hyderabad pilot versus production versus future

Scope	Required
Controlled Hyderabad pilot	One branch; production-grade identity provider; live catalogue/enquiry/CRM/quote/manual-or-gateway payment decision; Event Record; assignments; minimal operations/finance; audit; staging; support and rollback runbook
Full production	Complete role products, automated integrations, secure documents, monitoring/alerts, backup/restore drill, DB/E2E/security/load evidence, signed store releases, privacy/support processes
Future expansion	Additional branches/cities, advanced analytics, AI, marketplace ranking and multi-tenant/SaaS options only after the core is stable

10. Customer Module Map

The final navigation is **Home → Explore → Enquire → Plan → Profile**. “Enquire” is the transaction/work-history centre; “Plan” is the preparation/basket experience.

C-01 — Customer Home

Field	Detail
Purpose / users	Give a customer a trustworthy starting point and resume active work.
Screens	Home feed, occasion rail, services, upcoming-event/resume card, final action panel.
Actions	Browse, search, open occasion/service, resume enquiry/event, start planning.
Data / database	Catalogue occasions/services/media; customer enquiries/bookings/events. Tables exist.
API	Catalogue/search and own enquiry/booking/event APIs exist; current UI still uses sample/fallback paths.
Permissions	Public catalogue read where allowed; customer can read only own business records.
Status / dependencies	BROKEN / PARTIAL — UI exists; 20 Home widget tests fail. Depends on STAB-01 and live catalogue mapping.
Testing	Analyzer passes; Home tests fail across ordering, limits, scrolling, text scale and fallback icons.
Definition of Done	Live data, loading/empty/error/offline states, no invalid assets/overflow, all Home tests and one device E2E pass.

C-02 — Customer Explore

Field	Detail
Purpose / users	Let customers discover event types and services without exposing vendor base prices.
Screens	Explore, search, category/subcategory, service detail, favorites.
Actions	Search/filter, view approved content, favorite, add to Plan/Enquire.
Data / database	Managed catalogue hierarchy, media and customer-safe pricing/content. Catalogue tables exist.
API	Catalogue/search endpoints exist; customer-safe response review and pagination need E2E proof.
Permissions	Public/customer reads; internal vendor price and notes must never be returned.
Status / dependencies	PARTIAL — broad screens exist, but sample/fallback data, invalid images and one navigation TODO remain.
Testing	Unit/widget coverage is incomplete; no API/database/E2E catalogue proof.
Definition of Done	All approved catalogue data is live, customer-safe, searchable and resilient; accessibility, paging and E2E pass.

C-03 — Customer Enquire

Field	Detail
Purpose / users	First-class place to submit and track enquiries, quotations and booking conversion.
Screens	Enquiry inbox/history, composer/checkout, success, detail, quotation detail, payment submission.
Actions	Create/submit, view status, approve/reject/request quote revision, submit advance reference.
Data / database	<code>enquiries</code> , enquiry items/services, <code>crm_leads</code> , <code>quotations</code> , <code>payments</code> , <code>bookings</code> , activities/timelines.
API	Enquiry create/read, quotation own actions, payment submit/read and booking read exist.
Permissions	<code>enquiry.*_own</code> , <code>quotation.*_own</code> , <code>payment.*_own</code> , <code>booking.read_own</code> ; backend ownership checks required.
Status / dependencies	PARTIAL — connected foundation exists; navigation is in the wrong order/name and payment/PDF are placeholders.
Testing	Backend unit workflow exists; real Postgres, API and mobile E2E are missing.
Definition of Done	Final nav and history work; duplicate submission is idempotent; real quote document/payment strategy is implemented; ownership denial and E2E pass.

C-04 — Customer Plan

Field	Detail
Purpose / users	Help a customer assemble event requirements before creating an enquiry.
Screens	Plan basket, event details, selected services, budget/preferences and review.
Actions	Add/remove/edit items, save draft, continue to Enquire.
Data / database	Local plan state plus enquiry snapshot on submit; no disconnected permanent plan database should be invented without need.
API	Uses catalogue reads and enquiry command when submitted; draft-sync behavior is an open product choice.
Permissions	Customer-only draft/own data; server validates submitted catalogue identifiers and limits.
Status / dependencies	PARTIAL — screens exist; target nav moves Plan after Enquire. Depends on OD-01 and C-02/C-03 contracts.
Testing	Cache migration tests pass; complete persistence/recovery/E2E missing.
Definition of Done	Draft survives intended lifecycle, validates all inputs, submits exactly once and transitions clearly into C-03.

C-05 — Customer Profile

Field	Detail
Purpose / users	Manage the customer account, sessions, preferences and support access.
Screens	Profile/account, role switch where eligible, favorites, session/logout, help/privacy.
Actions	View/update permitted profile fields, manage session, switch approved role, logout, request support.
Data / database	<code>app_users</code> , role assignments, device sessions and customer profile/preferences where implemented.
API	Identity/bootstrap/session APIs exist; full profile/preferences/privacy endpoints are incomplete.
Permissions	Own account only; role switching only to an active verified assignment.
Status / dependencies	PARTIAL — current tab is "Account"; notifications/support/profile completeness is limited.
Testing	Auth unit tests exist; device/session/profile E2E and privacy tests missing.
Definition of Done	Renamed Profile, secure own-data edits, session/device controls, role rules, help/privacy and logout E2E pass.

11. Vendor Module Map

V-01 — Vendor Home

Field	Detail
Purpose / users	Give approved vendor owners/members today's assignments and urgent actions.
Screens	Dashboard, status cards, upcoming work and alerts.
Actions	View assigned work, respond, open progress, see payment summary where permitted.
Data / database	Vendor profile, role link, assignments, events, progress and settlement summaries. Existing foundation tables.
API	Vendor own dashboard/assignment APIs exist.
Permissions	Vendor owner/member own or assigned records only.
Status / dependencies	PARTIAL — live operations dashboard exists; onboarding/availability/notification dependencies are incomplete.
Testing	Focused API/widget/E2E coverage incomplete.
Definition of Done	Approved vendor sees only own live work, safe empty/error states, due alerts and device E2E.

V-02 — Vendor Work Orders

Field	Detail
Purpose / users	Receive, accept/reject and execute event service assignments.
Screens	Work-order list/detail, response, progress, evidence, delivery/completion.
Actions	Accept/reject, update status, add note/proof, mark completion subject to verification.
Data / database	<code>vendor_assignments</code> , event/vendor notes, progress, evidence/storage, Event Record.
API	Assignment list/detail/update/reject/progress endpoints exist; secure binary evidence pipeline is missing.
Permissions	<code>vendor_work_order.*_assigned</code> , <code>vendor_evidence.submit_assigned</code> , operations assigned capabilities.
Status / dependencies	PARTIAL — assignment/progress works at foundation level; complete work-order contract and dispute/acceptance target missing.
Testing	Unit foundations exist; real DB, evidence security and E2E missing.
Definition of Done	State machine approved, concurrent updates safe, proof protected, customer/internal fields filtered, full happy/unhappy E2E passes.

V-03 — Vendor Catalogue

Field	Detail
Purpose / users	Let verified vendors maintain offerings and submit internal prices for Mee Events review.
Screens	Listings, listing editor, variants/media, price proposal, availability, review status.
Actions	Create draft, edit, submit for review, respond to revision, manage availability.
Data / database	Vendor/category foundation exists; full applications/listings/versions/variants/price-review entities are incomplete or missing.
API	Profile/category/assignment APIs exist; complete vendor listing/review APIs are MISSING .
Permissions	Vendor manages own drafts/base price; Mee Events approves customer price/visibility.
Status / dependencies	MISSING / PARTIAL backend foundation. Depends on managed-marketplace ADR, files and approval workflow.
Testing	Missing module-level test suite.
Definition of Done	Application/KYC approval, versioned listing, protected base price, review/audit, availability and customer-safe publication work end to end.

V-04 — Vendor Earnings

Field	Detail
Purpose / users	Show vendor bills, settlements and payment status without exposing unauthorized finance data.
Screens	Earnings summary, work-order amount, invoice submission, settlement detail/history.
Actions	View own amounts, submit invoice/document, track settlement/dispute where approved.
Data / database	Vendor bills/settlements, finance summary, payments and private documents. Foundation exists.
API	Vendor payment read capability and finance settlement APIs exist; vendor self-service UX/API proof incomplete.
Permissions	Vendor own financial records only; finance/manager approval remains server-controlled.
Status / dependencies	PARTIAL. Depends on files, approval/reconciliation and approved settlement target states.
Testing	Ownership/field-filter/integration/E2E missing.
Definition of Done	Amounts reconcile to Event Record, documents are protected, state/audit is complete and vendor cannot see other vendors.

V-05 — Vendor Profile

Field	Detail
Purpose / users	Vendor application, identity, KYC, categories, availability, team and quality profile.
Screens	Application, KYC, business profile, documents, categories, availability, members, reviews/quality, session.
Actions	Apply, upload, edit permitted fields, manage team/availability, view verification.
Data / database	Vendor/profile/category/bank foundation exists; application/KYC workflow and reviews are incomplete.
API	Vendor create/update/own APIs exist for employees/vendor; application and secure document endpoints missing.
Permissions	Own profile edits; verification/suspension and visibility only by authorized employees.
Status / dependencies	PARTIAL. Depends on storage, review workflow, consent/retention and role-assignment issuance.
Testing	KYC privacy, authorization, file and E2E tests missing.
Definition of Done	Application-to-approved-role flow is auditable, KYC protected, field-level permissions enforced and review/appeal rules approved.

12. Worker Module Map

W-01 — Worker Home

Field	Detail
Purpose / users	Show an approved worker today's tasks, attendance state and urgent actions.
Screens	Dashboard, today/upcoming work, check-in prompt and alerts.
Actions	Open task, accept/reject, check in/out, update progress.
Data / database	Worker, tasks/assignments, attendance, events and payout summary. Existing foundations.
API	Worker own dashboard/task/attendance operations exist.
Permissions	Worker own/assigned records only.
Status / dependencies	PARTIAL — dashboard/task UX exists; full availability, earnings and alerts absent.
Testing	Unit/widget/E2E incomplete.
Definition of Done	Worker sees only current authorized work, clear shift state and offline/error handling; device E2E passes.

W-02 — Worker Tasks

Field	Detail
Purpose / users	Execute assigned event duties with traceable status, notes, evidence and incidents.
Screens	Task list/detail, response, progress, proof, issue/blocker and completion.
Actions	Accept/reject, travel/check-in/start/update/complete, add proof/issue.
Data / database	<code>worker_tasks</code> , assignments, operations tasks, issues/photos, Event Record, timelines.
API	Worker task response/progress and operations issue/photo foundations exist; secure evidence is missing.
Permissions	Assigned worker only; manager verifies/changes controlled states.
Status / dependencies	PARTIAL — task detail and progress exist; proof/incidents and normalized target states need design.
Testing	State/authorization/integration/device E2E missing.
Definition of Done	Approved state machine, offline retry/idempotency, protected evidence, manager visibility and full E2E pass.

W-03 — Worker Attendance

Field	Detail
Purpose / users	Record event work attendance separately from task outcome or performance.
Screens	Attendance status, check-in/out, history, exception/correction request.
Actions	Check in/out, attach permitted location/proof, request correction.
Data / database	Worker attendance logs and operations attendance; GPS fields are currently placeholders.
API	Check-in/out foundations exist. Location policy and correction approval APIs are incomplete.
Permissions	Worker own attendance; authorized operations/manager corrections with reason/audit.
Status / dependencies	PARTIAL / RISKY — privacy, consent, accuracy, offline and anti-abuse rules are not complete.
Testing	Time-zone, replay, location privacy, correction and E2E tests missing.
Definition of Done	Approved privacy policy, server timestamps, idempotent check-in/out, audited corrections and device tests pass.

W-04 — Worker Earnings

Field	Detail
Purpose / users	Show assigned-work payout inputs and payout status.
Screens	Earnings summary, task/event breakdown, payout detail/history.
Actions	View own earnings/payouts and raise a supported discrepancy.
Data / database	Worker payouts and finance summaries exist.
API	Worker payment-read capability and finance payout APIs exist; self-service contract/UX incomplete.
Permissions	Own payout data only; approval/payment only finance capabilities.
Status / dependencies	PARTIAL . Depends on payout calculation policy, approval and reconciliation.
Testing	Calculation, privacy, integration and E2E missing.
Definition of Done	Approved calculation source, reconciliation, audited adjustments and strict own-record filtering pass.

W-05 — Worker Profile

Field	Detail
Purpose / users	Worker application, approval, skills, availability, emergency/payment profile and account.
Screens	Application, identity/documents, skills, availability, bank/UPI masked fields, profile/session.
Actions	Apply, update permitted fields, upload documents, set availability, view approval.
Data / database	Worker/skills/bank foundation exists; application/availability workflow and protected documents incomplete.
API	Worker create/update/own APIs exist; self-application/review/storage gaps remain.
Permissions	Own permitted fields; approval/suspension only authorized employee; sensitive fields masked.
Status / dependencies	PARTIAL. Depends on identity proof, storage, review, retention and role-assignment rules.
Testing	Privacy/authorization/file/E2E missing.
Definition of Done	Application-to-active-role is secure/auditable, documents protected, skills/availability usable and sensitive data masked.

13. Employee Mobile Module Map

Current fact: no `apps/employee-mobile` Flutter package, no `employee_mobile` bootstrap surface and no store/release shell exist. All EM modules are **PLANNED — NOT IMPLEMENTED**. Existing manager/operations Flutter screens may be extracted only after dependency and security review.

EM-01 — Home / My Work

Field	Detail
Purpose / users	Mobile-first start for authorized employees: today, due, overdue, events, approvals and alerts.
Screens	Role-aware home, My Work, due/overdue sections, quick actions.
Actions	Open assigned record/task, prioritize today, acknowledge work.
Data / database	Existing leads/events/tasks plus proposed common work projection; generic work model not yet approved.
API	Existing CRM/manager/operations reads can seed projections; a safe employee-mobile bootstrap/My Work endpoint is missing.
Permissions	Capability + branch + assignment/team scope; never “all employees see all.”
Status / dependencies	BLOCKED / MISSING — OD-02, OD-03 and OD-04.
Testing	None.
Definition of Done	Sales-person slice shows only authorized, real, ordered work and updates from web/mobile remain consistent.

EM-02 — Tasks / Assignments

Field	Detail
Purpose / users	Execute assigned work away from a desktop.
Screens	Task queue/detail, accept/start/update/block/complete, notes/evidence/history.
Actions	Acknowledge, start, record activity/outcome/next action, block/escalate, complete.
Data / database	Existing event/operations tasks; proposed work item if approved; activity, evidence, outbox/audit.
API	Event/operations task APIs exist; generic employee work and escalation APIs missing.
Permissions	Assignee edits own execution fields; assign/verify/override only named capabilities.
Status / dependencies	MISSING ; depends on common work-state decision and secure files/notifications.
Testing	None.
Definition of Done	One role's task lifecycle works mobile ↔ API ↔ DB ↔ manager web with audit, offline/idempotency and denial tests.

EM-03 — Leads / Customers

Field	Detail
Purpose / users	Give permitted sales/CRM staff assigned lead and customer context.
Screens	My Leads, lead detail, customer summary, enquiry/quote status and activity.
Actions	Claim/update within capability, record contact, view requirements and quotation state.
Data / database	CRM leads, enquiries, users/customer profile, lead activities and quotations.
API	CRM lead list/detail/claim/update exists; assignment-scoped mobile projection/customer 360 is incomplete.
Permissions	Existing <code>crm_lead.*</code> , <code>crm_customer.read</code> ; assignment/team scope must be enforced.
Status / dependencies	MISSING UI / PARTIAL API . Sales-person is the first recommended employee-mobile role.
Testing	Backend unit foundations exist; mobile/API/E2E and data-minimization tests missing.
Definition of Done	Assigned salesperson can safely complete lead-detail work without seeing unauthorized customer records.

EM-04 — Follow-up / Communication

Field	Detail
Purpose / users	Record calls/outcomes and always create the next action when required.
Screens	Due queue, lead communication sheet, outcome, schedule next action, overdue queue.
Actions	Start/log call, choose outcome, add note, set next due action, complete/escalate.
Data / database	<code>lead_activities</code> partially represents calls/follow-up; no normalized work lifecycle or provider messaging record.
API	Lead requirements/activity behaviors exist; dedicated due queue/outcome/next-action APIs are missing.
Permissions	Assigned sales/telecaller plus manager team scope; call/contact data is private.
Status / dependencies	MISSING / BLOCKED by OD-04 and communication/consent choices.
Testing	None for full lifecycle.
Definition of Done	Due/overdue is server-derived, every activity is attributable, next action is consistent and manager sees SLA outcome.

EM-05 — Approvals

Field	Detail
Purpose / users	Allow only authorized managers/finance staff to make small mobile-safe decisions.
Screens	Pending approvals, detail/evidence, approve/reject reason and history.
Actions	Review, approve/reject with reason, request more information.
Data / database	Existing finance/manager actions and audit; no unified approval inbox model found.
API	Some approval capabilities/endpoints exist; common approval projection is missing.
Permissions	Exact capability plus scope and valid state; high-risk/bulk reconciliation remains web-only.
Status / dependencies	MISSING / PARTIAL backend. Depends on approved approval types and secure documents.
Testing	Authorization/state/concurrency/E2E missing.
Definition of Done	Approved types only, complete context, reason/audit, double-action protection and web/mobile consistency.

EM-06 — Notifications

Field	Detail
Purpose / users	Deliver assignment, due, overdue, escalation, approval and business-change alerts.
Screens	Inbox, detail/deep link, preferences and read state.
Actions	Open, mark read, follow deep link, manage allowed preferences.
Data / database	Outbox events exist; notification inbox/device-token/preference model is incomplete.
API	No complete mobile notification delivery/inbox contract.
Permissions	Only recipient's notifications; payload must minimize sensitive data.
Status / dependencies	MISSING ; depends on provider, token lifecycle, retries and escalation policy.
Testing	None for delivery.
Definition of Done	Reliable provider delivery, deduplication, deep links, read state, retry/dead-letter monitoring and privacy tests pass.

EM-07 — Team / Manager View

Field	Detail
Purpose / users	Give authorized managers workload, overdue, exceptions and outcomes—not employee surveillance.
Screens	Team work, overdue/escalations, event health and selected metrics.
Actions	Filter team, reassign where permitted, review/verify, intervene/escalate.
Data / database	Tasks/leads/events plus proposed hierarchy/team scope and work outcomes. Hierarchy is missing.
API	Manager dashboards/tasks exist for events; company/team work projection is missing.
Permissions	<code>manager_*</code> , assignment/report capabilities plus approved team scope; finance hidden unless authorized.
Status / dependencies	MISSING / BLOCKED by employee hierarchy and work-item decisions.
Testing	None for complete team scoping.
Definition of Done	Manager sees only authorized team, workload and SLA/outcome signals are auditable, and access-denial tests pass.

EM-08 — Employee Profile

Field	Detail
Purpose / users	Show employee identity, active role/capabilities, account/session and support.
Screens	Profile, role/scope, devices/sessions, settings, help/privacy/logout.
Actions	View permitted data, switch assigned role, revoke/logout and contact support.
Data / database	App users, role assignments and device sessions exist; employee profile/hierarchy model missing.
API	Identity/bootstrap/session exists; employee-specific profile and device management incomplete.
Permissions	Own profile/session; role assignment only administrator.
Status / dependencies	MISSING UI / PARTIAL identity API.
Testing	Auth foundation tests exist; employee device/app E2E missing.
Definition of Done	Only active employees enter, role/scope is server-derived, revoked sessions stop immediately and store privacy requirements are met.

14. CRM Module Map

CRM-01 — Lead / Enquiry Inbox

Field	Detail
Purpose / users	Receive customer enquiries as leads and control ownership/SLA.
Screens	Lead list, filters, lead detail and claim/assignment controls.
Actions	View, claim, assign where permitted, update status/requirements.
Data / database	enquiries , CRM leads, activities, users and branch.
API	Lead list/detail/claim/update foundation exists.
Permissions	crm_lead.read/update ; assignment only crm_lead.assign ; record/team scope needs stronger proof.
Status / dependencies	PARTIAL — live pages exist; queue assignment, SLA and E2E completeness missing.
Testing	Backend unit specs pass; ERP component/E2E and real DB missing.
Definition of Done	No lead is lost/duplicated, ownership is scoped/audited, SLA clock is visible and API+browser E2E pass.

CRM-02 — My Work

Field	Detail
Purpose / users	Give each employee one prioritized queue across leads/follow-ups/tasks.
Screens	Today, due, overdue, upcoming and completed.
Actions	Open, acknowledge/start, record outcome/next action and complete.
Data / database	Existing lead activities/event tasks are fragmented; generic work model missing.
API	No unified My Work API found.
Permissions	Own assignments; managers use explicit team scope.
Status / dependencies	MISSING / BLOCKED by OD-04.
Testing	None.
Definition of Done	One authoritative work queue drives web and employee mobile, with due/SLA/escalation and audit proof.

CRM-03 — Follow-up

Field	Detail
Purpose / users	Schedule, execute and measure lead/customer follow-up.
Screens	Due queue, activity composer, outcomes, next action and overdue view.
Actions	Log call/message/note, set result, schedule next action, escalate.
Data / database	Lead activities and first-response fields partially exist; normalized lifecycle missing.
API	Lead activity/requirements foundation only; due/outcome/escalation contract missing.
Permissions	Assigned staff and scoped manager; private communications protected.
Status / dependencies	PARTIAL data / MISSING product. Depends on OD-04 and channel/consent policy.
Testing	Full workflow missing.
Definition of Done	Server-derived due/overdue, immutable activity history, valid next action and SLA reporting work end to end.

CRM-04 — Customer 360

Field	Detail
Purpose / users	Authorized staff see one customer relationship across enquiries, quotes, bookings, events and activity.
Screens	Customer summary, contact, timeline, enquiries, quotes, bookings/events and notes.
Actions	View linked history, add scoped note, open related work.
Data / database	Relationships exist across users/enquiries/leads/quotes/bookings/events; a unified projection is missing.
API	Individual APIs exist; customer-360 aggregation/filtering endpoint missing.
Permissions	<code>crm_customer.read</code> plus branch/record scope and field minimization.
Status / dependencies	MISSING UI/API projection.
Testing	Privacy/aggregation/browser E2E missing.
Definition of Done	One linked identity, no copied records, strict field filtering and complete timeline reconciliation pass.

CRM-05 — Pipeline

Field	Detail
Purpose / users	Manage lead progression and exceptions through approved states.
Screens	Kanban/list, filters, ageing and stage detail.
Actions	Move only through valid transitions, assign, filter and inspect ageing.
Data / database	Lead statuses exist; target names differ and transition policy needs approval.
API	Lead updates exist; explicit transition policy/metrics incomplete.
Permissions	Update assigned/scoped leads; assignment/override only manager capability.
Status / dependencies	PARTIAL. Depends on approved lead state machine.
Testing	Transition, concurrency and browser E2E missing.
Definition of Done	Approved transitions enforced server-side; ageing/SLA correct; lost reason and conversion link are auditable.

CRM-06 — Quotations

Field	Detail
Purpose / users	Prepare, review, send, revise and convert controlled quotations.
Screens	Quote list/detail/editor, version/revision, approval/send and customer status.
Actions	Draft/edit/send/revise; customer approve/reject/revision; employee conversion.
Data / database	Quotations/items/documents/activities and links to lead/enquiry/payment.
API	Broad quotation APIs exist. Real internal approval, PDF and secure delivery are incomplete.
Permissions	CRM quotation read/manage; customer own actions; approval boundaries need final policy.
Status / dependencies	PARTIAL / PLACEHOLDER PDF.
Testing	Backend workflow passes with fakes; PDF/storage/DB/browser/mobile E2E missing.
Definition of Done	Versioned amounts, approved state machine, protected PDF, customer action, audit and conversion E2E pass.

CRM-07 — Team Management

Field	Detail
Purpose / users	Managers assign work and balance team workload.
Screens	Team roster, workload, unassigned/overdue and reassignment history.
Actions	Assign/reassign within scope, inspect capacity and escalations.
Data / database	Roles exist; employee hierarchy/team/department model missing.
API	Lead assign capability exists; team/workload APIs missing.
Permissions	Manager scoped team only; administrator manages role assignments.
Status / dependencies	MISSING / BLOCKED by OD-03/OD-04.
Testing	None.
Definition of Done	Approved hierarchy and capacity rules, no cross-team leakage, every assignment/reassignment audited.

CRM-08 — Targets & Performance

Field	Detail
Purpose / users	Compare approved targets with real activity and business outcomes.
Screens	Personal/team targets, response SLA, conversion/outcome and trends.
Actions	View; authorized managers configure approved target periods.
Data / database	Targets/departments/campaigns not found; events/leads can supply outcomes later.
API	Missing.
Permissions	Self/team/company views by explicit reporting capabilities.
Status / dependencies	MISSING / DEFERRED until work and CRM data are reliable.
Testing	None.
Definition of Done	Metric definitions approved, calculations reproducible, attendance/login not confused with outcome, access and reconciliation tests pass.

CRM-09 — Reports

Field	Detail
Purpose / users	Report lead sources, SLA, pipeline, conversion and sales outcomes.
Screens	Standard report catalogue, filters, drill-down and controlled export.
Actions	View/filter/export only as authorized.
Data / database	Transactional data exists; report projections/definitions incomplete.
API	General CRM reporting endpoints not found.
Permissions	Explicit report capability and row/field scope; export is audited.
Status / dependencies	MISSING / DEFERRED.
Testing	Reconciliation, authorization, performance and export tests missing.
Definition of Done	Approved metric dictionary, totals reconcile to source records and safe export/performance tests pass.

CRM-10 — Activity / Audit

Field	Detail
Purpose / users	Separate business activity ("work performed") from audit ("record changed").
Screens	Record activity timeline and restricted audit inspection.
Actions	Record permitted activity; view scoped history; auditors view immutable change evidence.
Data / database	Lead/module activities, timelines, append-only <code>audit_events</code> and outbox exist.
API	Narrow activity/audit foundations exist; unified presentation/filtering incomplete.
Permissions	Activity by actor/record scope; <code>audit.read</code> only auditor/administrator capability.
Status / dependencies	PARTIAL. Depends on work model and retention/redaction policy.
Testing	Append-only unit probes exist; DB immutability/authorization/browser tests missing.
Definition of Done	Activity and audit semantics are distinct, immutable where required, searchable, retained and strictly authorized.

15. ERP Module Map

ERP-01 — Event Control

Field	Detail
Purpose / users	Central Event Record after booking, linking planning, fulfilment and finance.
Screens	Event list/detail, status, program/notes/timeline/documents and linked modules.
Actions	View/update permitted fields, change valid state, add notes/milestones.
Data / database	<code>event_records</code> and related timelines/notes plus booking/assignments/inventory/finance.
API	Broad Event Record APIs exist.
Permissions	<code>erp_event.read/manage</code> , own customer tracking projection; state and field checks server-side.
Status / dependencies	PARTIAL / IMPLEMENTED — UNVERIFIED . Depends on real DB/E2E and target state approval.
Testing	Backend unit foundations pass; DB/browser cross-module E2E missing.
Definition of Done	Booking handoff is idempotent, linked modules reconcile, transitions/audit enforce policy and full event E2E passes.

ERP-02 — Manager Operations

Field	Detail
Purpose / users	Assign event managers, plan work and record progress.
Screens	Manager dashboard, event assignment, task list/detail and progress.
Actions	Assign/reassign manager, create/assign/update/complete task, add progress.
Data / database	Manager assignments, <code>event_tasks</code> , comments/progress/timelines.
API	Broad manager operations endpoints exist.
Permissions	<code>manager_event/task/progress/dashboard</code> capabilities plus scope.
Status / dependencies	PARTIAL — web routes and APIs exist; generic employee work/team hierarchy/mobile execution absent.
Testing	Unit foundations pass; real DB/team scope/browser/mobile E2E missing.
Definition of Done	Assignment/task/progress lifecycle is approved, scoped, audited and visible consistently on web and employee mobile.

ERP-03 — Vendor Operations

Field	Detail
Purpose / users	Register/verify vendors and assign fulfilment to Event Records.
Screens	Vendor registry/detail/create, event assignment, assignment detail and progress.
Actions	Create/update/verify, assign, monitor response/progress and close.
Data / database	Vendors/categories/bank, assignments, notes/progress and settlements.
API	Broad vendor management endpoints exist.
Permissions	<code>erp_vendor</code> / <code>crm_vendor</code> manage/read; vendor sees only own/assigned.
Status / dependencies	PARTIAL — operational registry/assignment foundation exists; application/listing/pricing/quality incomplete.
Testing	Unit foundation; DB/E2E/field-filter and full vendor workflow missing.
Definition of Done	Application-to-settlement lifecycle, internal price protection, assignment state, quality and audit pass end to end.

ERP-04 — Worker Operations

Field	Detail
Purpose / users	Register/approve workers and manage event duties/attendance.
Screens	Worker registry/detail/create, task/attendance and assignment monitoring.
Actions	Create/update/approve, assign task, monitor attendance/progress and payout input.
Data / database	Workers/skills/tasks/attendance/notes and payouts.
API	Broad worker management endpoints exist.
Permissions	<code>erp_worker</code> / <code>crm_worker</code> manage/read; worker only own assigned data.
Status / dependencies	PARTIAL — registry/tasks/attendance foundation; application/availability/quality/privacy incomplete.
Testing	Unit foundation; DB/E2E/privacy/location missing.
Definition of Done	Application-to-payout lifecycle, consent, assignment, attendance correction and strict data scope pass.

ERP-05 — Inventory

Field	Detail
Purpose / users	Track items, stock, custody, allocation, movement, return, damage and maintenance.
Screens	Inventory list/detail, warehouse, stock, allocations, movements, returns/damage/maintenance.
Actions	Create/update item, move/allocate/return, report damage and maintain.
Data / database	Extensive inventory/warehouse tables exist.
API	About 27 inventory and related warehouse handlers exist.
Permissions	Inventory/warehouse read/manage/allocate capabilities and branch scope.
Status / dependencies	PARTIAL / IMPLEMENTED — UNVERIFIED ; UI routes exist but transaction/E2E/custody proof incomplete.
Testing	Unit foundations; real DB concurrency/reconciliation/browser E2E missing.
Definition of Done	Stock cannot go inconsistent, custody chain and audit reconcile, concurrent allocation tests and event E2E pass.

ERP-06 — Procurement

Field	Detail
Purpose / users	Purchase required goods/services when inventory or fulfilment is insufficient.
Screens	Requisitions, approvals, suppliers, purchase orders, goods receipt and invoice matching.
Actions	Request, approve, order, receive, match and close/dispute.
Data / database	Inventory suppliers exist; purchase-order/line/goods-receipt product tables were not found.
API	MISSING as a complete procurement domain.
Permissions	Requester, approver, purchaser, receiver and finance duties must be separated.
Status / dependencies	MISSING / DEFERRED until inventory and approval rules are stable.
Testing	None.
Definition of Done	Approved segregation of duties, three-way reconciliation as required, audit and real DB/E2E pass.

ERP-07 — Finance

Field	Detail
Purpose / users	Track customer payments/refunds, expenses, invoices/receipts and vendor/worker settlements.
Screens	Finance dashboard, event finance, payments, refunds, expenses, invoices, receipts, settlements and ledger.
Actions	Record/approve/reconcile permitted transactions and issue documents.
Data / database	Broad finance tables and summaries exist.
API	About 26 finance handlers exist; real gateway/bank reconciliation and document pipeline absent.
Permissions	Finance capabilities; approvals/reports separated; sensitive fields filtered.
Status / dependencies	PARTIAL / HIGH RISK — foundation exists but money/document/reconciliation production proof missing.
Testing	Unit foundations; decimal/reconciliation/concurrency/security/E2E missing.
Definition of Done	Approved accounting rules, immutable audit, double-entry/reconciliation decision, gateway/manual controls and finance E2E pass.

ERP-08 — Approvals

Field	Detail
Purpose / users	Centralize controlled business decisions with reason, evidence and segregation.
Screens	Approval inbox, detail/evidence, decision/history and escalation.
Actions	Submit, approve/reject/request information, delegate only by policy.
Data / database	Some module-specific approvals/capabilities exist; unified approval model/inbox not found.
API	Partial module actions; complete approval contract missing.
Permissions	Exact approval capability, scope, state and self-approval restrictions.
Status / dependencies	MISSING / PARTIAL . Depends on approval catalogue and document security.
Testing	Authorization, segregation, concurrency and E2E missing.
Definition of Done	Every controlled decision has policy, eligible approver, evidence/reason, immutable audit and no double/self approval where prohibited.

ERP-09 — Administration

Field	Detail
Purpose / users	Manage users, roles, branch, catalogue/policy, feature flags and compliance.
Screens	Users/roles, assignments, branch/settings, catalogue review, providers, audit and feature controls.
Actions	Grant/revoke scoped roles, configure approved policy and review audit.
Data / database	Users/roles/branch/catalogue/audit foundations exist; complete admin product absent.
API	Identity/platform/catalogue review foundations; admin orchestration incomplete.
Permissions	Administrator capabilities; auditor read only; high-risk changes require stronger controls.
Status / dependencies	PARTIAL backend / MISSING product.
Testing	Privilege-escalation, audit, recovery and browser E2E missing.
Definition of Done	Least privilege, protected high-risk actions, complete audit, safe defaults and admin recovery runbook pass.

ERP-10 — Reports

Field	Detail
Purpose / users	Operational and financial management reporting with traceable definitions.
Screens	Event/vendor/worker/inventory/finance/department reports and controlled exports.
Actions	View/filter/drill/export according to capability.
Data / database	Source transactions exist; approved reporting projections and metric dictionary incomplete.
API	Some dashboards/summaries exist; full reporting APIs missing.
Permissions	<code>report.operational.read</code> or <code>report.financial.read</code> ; row/field scope and export audit.
Status / dependencies	MISSING / PARTIAL summaries / DEFERRED.
Testing	Reconciliation, authorization, export and performance tests missing.
Definition of Done	Metrics reconcile to source, definitions/version are documented, access safe and production-size performance tested.

How to use this roadmap

Read **Sections 1–8** to understand where the project is now. Work only on the item named in **Section 29 — Exact Next Task**. When its exit gate is green, update the Master TODO and move to the next item in **Section 26 — Recommended Build Order**. Never mark a screen or API as done without UI → API → database → authorization → test evidence.

Status words used in this document

Status	Meaning
DONE	Implemented and verified by current evidence
IMPLEMENTED — UNVERIFIED	Code exists, but real database/device/end-to-end proof is incomplete
PARTIAL	Useful pieces exist; the whole module is not complete
PLACEHOLDER	Temporary or deliberately non-production behavior
BROKEN	Implemented behavior currently fails a required check
BLOCKED	Work cannot be completed until a named dependency or decision is resolved
MISSING	No implementation found
DEFERRED	Intentionally scheduled later

16. Employee Role Matrix

Actual platform roles and surfaces

This table uses the repository's current capability map. "Scoped" means the backend must also verify branch, assignment/team and record access. Sales Person, Telecaller, Marketing and General Manager are **not current platform roles**; they must not be invented in UI only.

Role	Application	Module	View	Create	Edit	Assign	Approve	Report	Mobile	Web
customer	CVW Mobile	Own enquiry/quote/booking/payment/event	Own	Enquiry/change	Own allowed actions	No	Own quote decision	No	Yes	No current customer web
vendor_owner	CVW Mobile	Own vendor/work orders/operations	Own/assigned	Proposal/evidence/invoice	Own/assigned	No	Accept/reject assigned	Own payment read	Yes	No current vendor web
vendor_member	CVW Mobile	Assigned work/own vendor	Own/assigned	Evidence/issues	Own/assigned	No	Accept/reject assigned	No	Yes	No current vendor web
worker	CVW Mobile	Own assignment/attendance/operations	Own/assigned	Attendance/issues/photos	Own duty	No	Respond to own assignment	Own payment read	Yes	No current worker web
employee	Employee system	CRM + broad ERP execution	Yes, broad	Many module records	Many module records	Task/ops paths	Payment operation exists	Dashboards, not explicit report capabilities	Planned	Yes
support	Employee system	CRM/customer/vendor/ops read/support update	Scoped	Limited	Lead update	No explicit assign	No	No explicit report	Planned if approved	Yes
finance	Employee system	Payments/finance/settlement/financial report	Scoped	Finance records	Finance records	No general assignment	Payment/refund/approval decisions	Financial	Planned if approved	Yes
manager	Employee system	CRM/ERP/manager/operations	Scoped	Broad operations	Broad operations	Lead/task/operations	Reads approval; finance boundaries limited	Operational	Planned	Yes
administrator	Employee system	All capability IDs	Yes	Yes	Yes	Yes	Yes	Yes	Decision required	Yes
auditor	Employee system	Read CRM/ERP/audit/catalog review	Read only	No	No	No	No	Operational + financial read	Usually no	Yes

Current employee capability groups

Role	Actual notable capabilities
employee	CRM lead/customer/quotation/booking/payment/vendor/worker/operations; Event Records; manager tasks; vendor/worker; inventory/warehouse; finance; operations. This is currently too broad for specialized employee personas.
support	CRM lead read/update, customer/vendor/operations read, event/manager/operations dashboards read.
finance	Customer/vendor/payment/event/vendor/worker reads; finance manage/settlement/dashboard; payment/refund approvals; approval decisions; financial reports.
manager	CRM lead update/assign; quotation/booking/payment; event/manager task; vendor/worker/inventory/warehouse; selected finance; operational reporting and operations management.
administrator	Every declared capability.
auditor	Read-only CRM/ERP/approval/report/audit/catalog review capabilities.

Target persona mapping — open until approved

Business persona	Recommended mapping method	Current truth
Sales Person	Narrow capability bundle + own assignment/team scope	Not an explicit role today
Telecaller	Narrow lead/follow-up bundle + queue assignment	Not an explicit role today
Sales Manager	Manager capability bundle + sales team scope	Not an explicit role today
Marketing staff/manager	Campaign/source/task bundles after domain exists	Campaign domain not present
Field/Event Manager	Manager/operations bundle + assigned events	Existing manager/ops capabilities can be reused
General Manager	Approved cross-department reporting/exception bundle	Not an explicit role today

Do not solve this by giving every employee the current broad **employee** role. Approve a capability-and-scope matrix, migrate safely, and test denial paths.

17. Employee Work Management

Current finding

No single generic company-wide Work Item model was found. Three related mechanisms exist:

1. `lead_activities` and lead first-response timestamps for CRM contact work;
2. `event_tasks` for manager/event planning;
3. operations tasks and task assignments for event execution.

They are real and useful, but they do not answer the complete cross-company questions: who assigned the work, due/overdue, outcome, next action, escalation, manager/team visibility and department performance.

Recommended decision process

Do not immediately create another `tasks` table. Write an ADR that compares:

- extending/generalizing one existing task aggregate;
- adding a generic `work_items` + `work_item_activities` /escalations layer that links to existing domain records;
- keeping domain tasks and building a unified read model/projection with a small orchestration record.


The recommendation is a generic work orchestration layer only if the ADR proves it prevents, rather than creates, duplication. Domain facts such as lead status and event task status must remain owned by their modules.

Minimum conceptual fields

Group	Fields
Identity	Work ID, work type, branch/department, related record type/ID
Responsibility	Assigned employee, assigned by, team/manager scope
Timing	Created, due, started, completed and SLA timestamps
State	Priority, status, blocked/escalation state
Result	Outcome, next action, notes and approved evidence links
Trace	Activity history, version, audit actor/request and outbox notification

Required workflow

Assignment

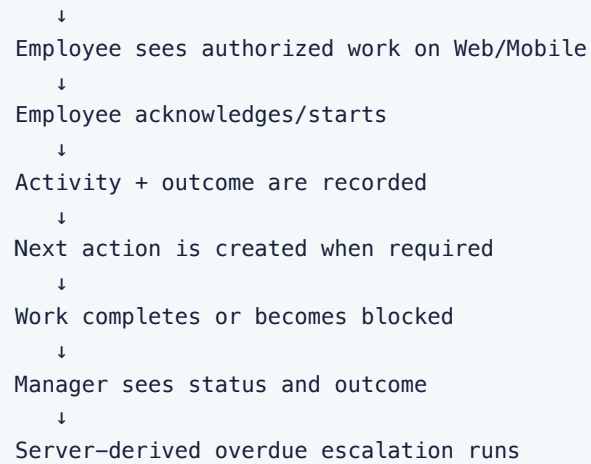

Rules

- Login is not work. Attendance is not task completion. Activity is not automatically a good outcome.
- Due/overdue must be calculated by the backend, not trusted from the phone clock.
- Every reassignment, override, approval and escalation needs reason and audit evidence.
- A notification informs; it never becomes the source of truth.
- Mobile and web update the same versioned work/business records.

18. Manager Monitoring / Performance

Signals that managers need

Signal	Question answered	Source
Assignment	What was assigned, to whom and by whom?	Work/assignment record + audit
Activity	What contact/update/work occurred?	Domain activity, not login logs
Timeliness	Was work started/completed by due time?	Server timestamps/SLA calendar
Outcome	What business result occurred?	Approved outcome on work/domain record
SLA	Was first response/next action achieved?	Lead/work SLA rules
Escalation	What is overdue/blocked and who was alerted?	Escalation record + outbox delivery
Performance	Did work produce expected quality/conversion/completion?	Approved metric dictionary; never guessed

Manager views

1. My events/work requiring attention.
2. Team workload: unassigned, due today, overdue and blocked.
3. Exceptions: SLA breach, rejected work, missing evidence and repeated failure.
4. Outcomes: conversion/completion/quality based on approved definitions.
5. Audit link: why a controlled record changed.

Do not build employee surveillance or infer performance from login time, phone location or raw activity count. Define fair metrics, privacy limits, retention and correction/appeal procedures first.


19. CRM ↔ ERP Data Flow

CRM and ERP are modules in the same employee web application and share the same backend/database. The handoff is a record transition, not a data copy.

Stage	CRM responsibility	ERP responsibility	Shared key/control
Enquiry	Receive customer intent and source	Read only when operationally needed	<code>enquiry_id</code>
Lead	Ownership, follow-up, requirements	No duplicate lead	<code>lead_id</code> linked to enquiry
Quotation	Price/version/customer decision	Uses approved commercial contract	<code>quotation_id</code>
Payment/Booking	Confirm approved payment policy and convert	Receives confirmed booking	<code>payment_id</code> , <code>booking_id</code>
Event Record	CRM shows linked conversion	ERP owns planning/execution aggregate	<code>event_record_id</code> linked to booking
Fulfilment	CRM sees customer-safe progress	ERP assigns manager/vendor/worker/inventory	Event-linked assignment IDs
Finance/Closure	CRM sees permitted customer/account state	ERP settles and closes	Event/finance IDs + audit

Required proof: creating or updating a stage never creates a parallel disconnected customer, quote, booking or event record; retries are idempotent; authorization and optimistic version checks reject stale/unauthorized writes.

20. Customer → CRM → ERP → Vendor/Worker Business Flow

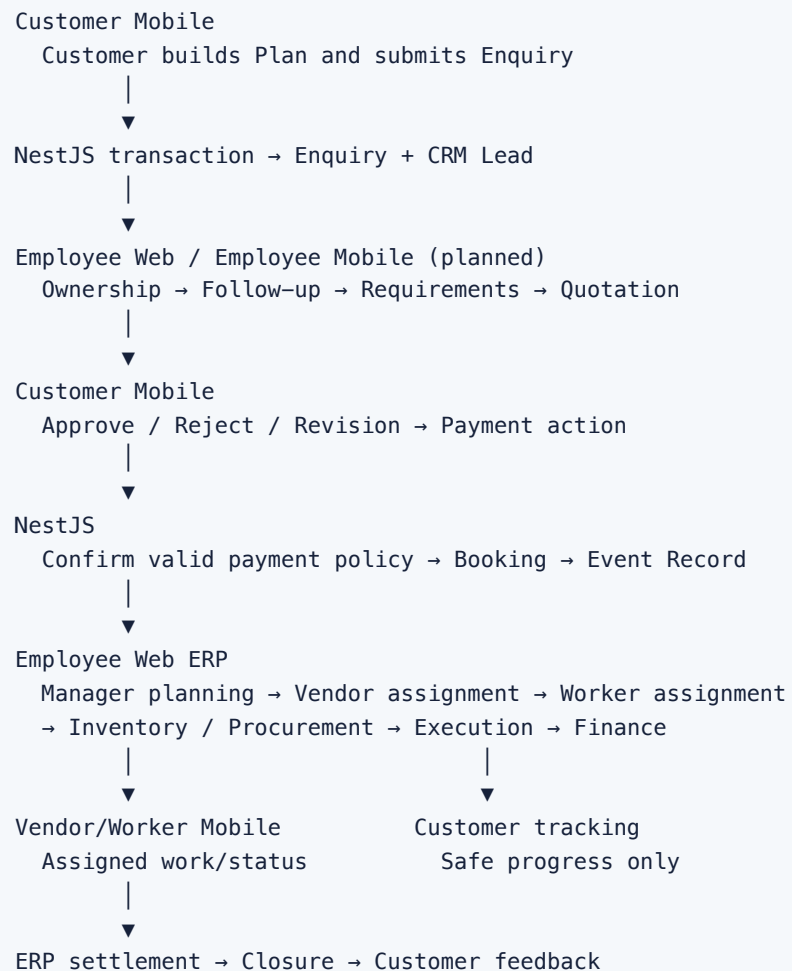

Stage	Primary interface	Current status
Plan/Enquiry	Customer Mobile	PARTIAL
Lead ownership/requirements	CRM Web	PARTIAL

Stage	Primary interface	Current status
Follow-up/My Work	CRM Web + future Employee Mobile	MISSING/PARTIAL data
Quote/customer decision	CRM Web + Customer Mobile	PARTIAL
Payment/booking	Customer Mobile + CRM/Finance Web	PLACEHOLDER/PARTIAL
Event Record	ERP Web	PARTIAL
Manager planning	ERP Web; future Employee Mobile execution	PARTIAL
Vendor/worker assignments	ERP Web + CVW Mobile	PARTIAL
Inventory/operations/finance	ERP Web	PARTIAL foundations
Procurement	ERP Web	MISSING
Closure/feedback	ERP + Customer Mobile	PARTIAL/MISSING

21. Status Machines

The left column is code truth. The right column is product intent from the requested roadmap. Do not rename or migrate states without an approved transition/migration plan.

Domain	Current implementation	Target state / gap
Enquiry	draft → submitted → received → contact_pending → in_discussion → proposal_expected → closed/cancelled	Confirm ownership of transitions and mapping to first-class Enquire UI.
Lead	new → claimed → contacted → qualified → quoted → converted/lost/closed	Intended wording says Quotation and Won/Lost. Recommend keep stable codes, define display labels, allowed transitions and lost/closed reasons.
Quotation	draft → sent → revision_requested → approved/rejected/expired/superseded	Target adds Internal Approval and Revised. Decide approval policy and version transition.
Payment	pending → paid/failed/refunded	Target says Created/Pending/Confirmed/Failed/Expired/Refunded. Decide gateway/manual semantics; do not equate operator entry with settled money.
Booking	confirmed/cancelled	Target says Pending Confirmation/Confirmed/In Planning/In Progress/Completed/Cancelled. Recommend booking remain commercial contract and Event Record own operational states unless business approves expansion.
Event Record	created → planning → requirements_confirmed → quotation_approved → booking_confirmed → manager_assigned → vendor_assigned → worker_assigned → preparation → ready → event_running → completed → settlement_pending → closed/cancelled	Strong current lifecycle; approve transition matrix, skip rules and compensations.
Event/manager task	pending → planning → assigned → in_progress → completed/cancelled	Target says Assigned/Acknowledged/In Progress/Blocked/Completed/Verified. Decide common work model before change.
Vendor assignment	invited → assigned → accepted/rejected → planning → travelling → on_site → working → completed/cancelled	Target work order adds Draft/Offered/Delivered/Accepted/Disputed. Reconcile commercial work-order acceptance and execution assignment.
Worker task	assigned → accepted/rejected → travelling → checked_in → working → completed → checked_out/cancelled	Add blocked/verified only if operational policy requires them; preserve attendance distinction.
Operations task	Event-task-like pending/planning/assigned/in-progress/completed/cancelled	Reconcile with Event Task/common Work Item to prevent duplicate semantics.
Finance settlement	open → partially_settled → settled → closed	Target calculated/reviewed/approved/paid/reconciled/disputed needs explicit accounting/approval policy.
Vendor settlement	pending → partially_paid → paid/cancelled	Add reviewed/approved/reconciled/disputed only after finance design.
Worker payout	pending → approved → paid/cancelled	Add calculation/reconciliation/dispute policy if required.

For each transition implement: allowed actor/capability, record scope, precondition, concurrency/version check, side effects, audit/outbox, idempotency and tests.

22. Permissions / Security

What is strong today

- E.164 OTP challenge with hashed/keyed verification material, expiry, resend/attempt/rate limits.
- Short access tokens, rotating opaque refresh tokens, device sessions and revocation/reuse response.
- Global authenticated principal, active role/assignment and branch context.
- Server capability guard and module-level domain checks.
- Append-only audit pattern, request ID and log redaction.
- Production refuses local OTP and validated secrets are expected.

What must be fixed before production

Risk	Required action
OTP provider placeholder	Implement approved provider, webhook/delivery handling, abuse monitoring, tests and recovery.
Broad employee role	Approve narrower capability bundles and assignment/team/record scopes.
Direct mobile Supabase	Remove direct DB dependency/asset secrets after usage proof; backend only.
Client-side web gate	Threat-model routes; ensure every API is authoritative, then add robust portal session/route protections.
Idempotency unused	Apply keys/replay behavior to enquiry, payment, booking, assignments and other critical creates.
File/storage placeholder	Private buckets/objects, server-issued upload/download, type/size/content checks, signed expiry, retention and audit.
Payment placeholder	Provider signatures/webhooks, amount/order matching, replay protection, reconciliation/refund controls—or explicitly controlled pilot manual process.
Notifications	Minimize payload, secure device tokens, retry/dead-letter, unsubscribe/preferences and audit delivery.
Rate limits in memory	Decide shared Redis-backed enforcement before multiple backend replicas.
Sensitive data	Define field-level responses, encryption/provider controls, masking, retention, export and deletion/legal policy for customer, employee, vendor, finance, KYC and location data.

Four checks for every protected action

1. Who is the authenticated user and active session?
2. Does the active role have the exact capability?

3. Does the user have branch/team/assignment/record access?

4. Is the action valid in the current record state and version?

Hidden buttons are usability only; the NestJS command must enforce all four checks.

23. Testing Strategy

Current result by level

Level	Required proof	Current evidence	Status
1. Format/lint/analyze	Clean automated static gate	TypeScript format/lint fail; Flutter analyze passes	BROKEN
2. Unit tests	Domain, auth, state and calculations	Backend 173 tests and ERP 2 tests pass	PARTIAL
3. Widget/component	UI states, accessibility and interactions	Flutter has 435 total results: 415 pass, 20 fail; ERP almost none	BROKEN/PARTIAL
4. Repository/database integration	Ordered migrations and real SQL transactions	None in CI; Docker unavailable during audit	MISSING/BLOCKED
5. API integration	Real Nest server + Postgres, auth and rollback	Demo scripts exist; no automated CI integration	MISSING
6. End-to-end	Customer/employee/vendor/worker journeys	No browser/device framework	MISSING
7. Security/performance	Abuse, authz, file/payment, load/concurrency	Unit foundations only; no production-scale suites	MISSING/PARTIAL
8. Operations/recovery	Deploy, monitoring, backup restore, rollback	Documentation exists; no live environment/drill	MISSING

Minimum test pyramid for every module

1. Pure unit tests for rules and state transitions.
2. Repository integration against a clean migrated PostgreSQL database.
3. Authenticated API happy path plus denial, invalid state, duplicate/retry and stale version paths.
4. Widget/component loading, empty, populated, error, offline and accessibility states.
5. One end-to-end role journey across UI → API → DB.
6. Audit/outbox companion-write assertions for controlled mutations.

Release gates

- Pull request: format, lint, typecheck/analyze, unit/widget, dependency/security checks.
- Merge/staging: clean migration, DB/API integration, browser/mobile smoke and artifact build.
- Release candidate: signed AAB/IPA, TestFlight/internal track, E2E, security/privacy review, monitoring and rollback.
- Production: approved change, backup/restore evidence, provider health and staged rollout.

24. App Store / Play Store Strategy

Store and privacy rules change. Verify the latest Google and Apple requirements during each release; this roadmap does not claim compliance.

Customer/Vendor/Worker app

Area	Current	Required
Android ID	Production <code>com.meevent.app</code> ; dev/staging flavors exist	Confirm permanent ID/ownership before publishing
Android signing	Release uses debug signing	Secure Play App Signing/upload key; release must fail without proper signing
Android artifact	CI debug dev APK only	Signed production AAB, internal/closed testing, staged rollout and rollback plan
iOS ID	<code>com.meeevents.meeEvents</code> found	Confirm final bundle ID, organization team, capabilities and environment separation
iOS signing	No production proof	Certificates/profiles or managed signing, archive validation and TestFlight
Version	<code>1.0.0+1</code>	Automated semantic/build numbering and release notes
API config	CI points to port 3000	HTTPS staging/production endpoints, certificate/network policy and no secret bundling
Observability	None proven	Privacy-approved crash reporting, logs/metrics and alert owner
Push/deep links	Not complete	Provider setup, token/deep-link tests and safe payloads
Privacy/store content	Not verified	Privacy policy, data safety/privacy nutrition answers, account/support/deletion processes, permissions justification and screenshots/metadata

Employee Mobile app

- Create a separate Flutter application only after OD-02 and shared-code boundaries are approved.
- Publish through Google Play and Apple App Store/TestFlight using organization-controlled accounts; APK may be used only for development/testing.
- Downloadability never grants employee access. OTP/session plus active employee role, capabilities, branch/team/record scope and revocation are mandatory.
- Prefer a role-by-role release: Sales Person → Telecaller → Manager → Field/Event Operations → selected roles.
- Keep detailed finance, bulk operations, configuration, reconciliation and large reports on employee web unless a specific mobile use case is approved.
- Use distinct app IDs, signing keys, push credentials, crash-reporting projects and store listings from the CVW app while sharing backend identity and business records.

CRM/ERP web production

Required: secure HTTPS host, separate staging/production environment and database, secrets manager, migration job, health checks, logs/metrics/traces, alerting, backups and restore drill, CSP/security headers, release/rollback and support ownership. None is proven live today.

Rollout sequence for both mobile apps

1. Developer signed debug builds.
 2. Automated test artifacts.
 3. Android internal track and iOS TestFlight internal group.
 4. Controlled Hyderabad pilot group with monitored production backend.
 5. Fixes and release-candidate sign-off.
 6. Staged production rollout with crash/API/business monitoring.
 7. Pause/rollback capability and documented incident response.
-

25. Master TODO

Priority: **P0** blocks safe work/release; **P1** required for Hyderabad pilot; **P2** required for full product; **P3** future enhancement. “Evidence” names what the audit actually found, not a claimed completion percentage.

ID	Application	Interface	Role	Module	Task	Pri	Status	Dependency	Evidence	Test status	Blocker	Next action	Definition of Done
STAB-01	Shared	Repo	All	Quality	Restore all current quality gates	P0	BROKEN	None	Format 280, lint 1, Flutter tests 20 fail	Red	Raw exports/test drift	Fix scoped issues and exclusions	Root verify + Flutter analyze/test green
STAB-02	Shared	Repo	All	Safety	Protect and classify dirty worktree	P0	PENDING	STAB-01	145 modified/add, 26 deleted, 102 untracked	N/A	Mixed changes	Group/review changes; no destructive reset	Every change owned, backed up and reviewable
STAB-03	Shared	Files	All	Cleanup	Remove only proven caches/junk/broken assets	P1	PENDING	STAB-02	~6.3 GiB regenerable; 24 invalid images; logs/.DS_Store	Rebuild required	Review asset replacements	Execute approved cleanup manifest	Rebuild/test passes; no needed evidence lost
STAB-04	Shared	Docs	All	Documentation	Correct counts, links, status and nav drift	P1	PARTIAL	STAB-01	Old test counts/nav/status; broken ADR link	Link check missing	None	Update canonical docs after decisions	Docs match source and links validate
CI-01	DevOps	CI	Developers	CI	Align branch and API port	P0	BROKEN	STAB-01	CI main ; repo master ; CI port 3000 vs backend 3002	CI unverified	Branch decision	Correct trigger/config and prove run	Push/PR execute intended jobs with correct endpoint
CI-02	DevOps	CI	Developers	CI	Add Postgres migration/integration job	P0	MISSING	DB-01	No DB service in CI	None	Integration harness	Create isolated clean DB job	Migrations + repository/API integration pass in CI
DB-01	Database	Postgres	System	Integration	Prove clean migrations 0001 – 0020	P0	BLOCKED	Docker/service	20 migrations/114 tables	Not run	Docker unavailable	Start DB, migrate twice, inspect schema	Clean apply, rerun behavior and rollback/recovery notes pass
DB-02	Database	Postgres	System	Integrity	Add critical idempotency use	P0	MISSING	DB-01	Table exists; no app use	None	Key policy	Design/apply to critical creates	Replay returns same result; conflicts rejected; tests pass
DB-03	Database	Postgres	Auditor	Audit	Prove append-only audit/outbox in real DB	P1	IMPLEMENTED — UNVERIFIED	DB-01	Tables/triggers/unit pattern probes	Fake-only	DB integration	Add real trigger/transaction tests	Mutation rollback/append-only/outbox atomicity proven
AUTH-01	Backend	API	All	Identity	Implement production SMS OTP provider	P0	PLACEHOLDER	Provider decision	External path returns 503	Unit foundation only	OD-06	Select/provider adapter/monitor/recovery	Staging delivery, abuse/expiry/retry and failure tests pass
AUTH-02	Backend	API	All	Sessions	Add distributed rate limit/abuse control	P1	PARTIAL	Redis/hosting decision	Limits exist; Redis unused	Unit only	Deployment topology	Implement shared counters if multi-replica	Cross-replica abuse test and monitoring pass
AUTH-03	Backend	API/Web/Mobile	Employees	Authorization	Approve employee capability/scope matrix	P0	BLOCKED	OD-03	Existing employee role broad	Guard unit tests	Business approval	Map personas to bundles/scopes	Least-privilege matrix approved and denial tests pass

ID	Application	Interface	Role	Module	Task	Pri	Status	Dependency	Evidence	Test status	Blocker	Next action	Definition of Done
AUTH-04	Mobile	Flutter	All	Data boundary	Remove direct Supabase client data path	P0	RISKY	Usage proof	.env bundled; service queries DB	No architecture test	OD-12	Trace usage, replace with Nest API	No direct DB credentials/client ; app functions/tests pass
C-01-T1	CVW Mobile	Customer	Customer	Home	Repair Home tests and live-data contract	P0	BROKEN	STAB-01	20 failed Home tests	415 pass/20 fail	UI/test drift	Fix behavior or approved test expectation	All target widths/text scales/scroll/data tests green
C-02-T1	CVW Mobile	Customer	Customer	Explore	Replace samples and invalid assets with approved catalogue	P1	PARTIAL	DB-01, files	Screens + fallback data + 24 bad images	Incomplete	Content/media review	Connect approved API and resilient image states	Live customer-safe catalogue E2E passes
C-03-T1	CVW Mobile	Customer	Customer	Enquire	Migrate final navigation/order and enquiry history	P1	PARTIAL	OD-01, STAB-01	Current Home/Explore/Plan/Enquiries/Account	Tests need update	OD-01	Approve mapping and implement focused slice	Home/Explore/Enquire/Plan/Profile and deep links pass
C-03-T2	Full stack	Customer/CRM	Customer/employee	Enquire	Prove enquiry → CRM lead real DB flow	P0	IMPLEMENTED — UNVERIFIED	DB-01, CI-02	Transaction code/demo scripts	Fake/unit only	Docker	Automate API integration	One enquiry/lead, audit/outbox, retry and authz proven
C-04-T1	CVW Mobile	Customer	Customer	Plan	Finalize draft persistence and submit boundary	P1	PARTIAL	C-02/C-03	Plan/cache code exists	Some cache tests pass	Draft product rule	Define local/server behavior	Recovery, validation and exactly-once submit tests pass
C-05-T1	CVW Mobile	Customer	Customer	Profile	Complete profile/session/privacy/support	P2	PARTIAL	AUTH-01	Account shell exists	E2E missing	Profile schema/policy	Specify permitted fields and device controls	Own-data/session/log out/privacy E2E passes
CRM-01-T1	CRM	Web	Employee/manager	Inbox	Complete assignment/SLA inbox	P1	PARTIAL	AUTH-03, DB-01	Lead list/detail/claim exists	Unit only	Team scope	Add unassigned/assigned/SLA views	Scoped claim/assign/SLA browser E2E passes
WORK-01	Backend/DB	API	Employee/manager	Work	Decide common employee work model	P0	BLOCKED	OD-04	Lead activities + two task systems	N/A	Architecture decision	Write ADR and migration/API plan	No duplicate authority; lifecycle/scope approved
CRM-02-T1	CRM/Employee Mobile	Web/Mobile	Employee	My Work	Build authoritative My Work projection	P1	MISSING	WORK-01	No unified queue	None	WORK-01	Implement first for Sales Person	Same scoped queue web/mobile; due/overdue tests pass
CRM-03-T1	CRM/Employee Mobile	Web/Mobile	Sales/telecaller	Follow-up	Build outcome/next-action/SLA lifecycle	P1	PARTIAL	WORK-01, AUTH-03	Lead activities partially cover calls/follow-up	Incomplete	Persona/channel policy	Implement server lifecycle and UI	Activity/outcome/next action/escalation E2E passes
CRM-04-T1	CRM	Web	Employee	Customer 360	Build linked customer projection	P1	MISSING	DB-01, AUTH-03	Source records linked separately	None	Field policy	Add filtered aggregate endpoint/view	Reconciles IDs; privacy and browser tests pass
CRM-05-T1	CRM	Web	Employee/manager	Pipeline	Approve/enforce lead transitions	P1	PARTIAL	Status decision	Status codes exist	Unit partial	Business transitions	Write matrix and command tests	Invalid transitions denied; reasons/conversion audited
CRM-06-T1	CRM	Web	Employee/manager	Quotation	Add internal approval/version policy	P1	PARTIAL	Approval decision	Draft/sent/revision/customer states exist	Unit foundation	State policy	Approve current-vs-target mapping	Version/approval/send/customer actions tested

ID	Application	Interface	Role	Module	Task	Pri	Status	Dependency	Evidence	Test status	Blocker	Next action	Definition of Done
CRM-07-T1	CRM	Web	Manager	Team	Add hierarchy/team scope/workload	P2	MISSING	AUTH-03, WORK-01	No employee hierarchy tables	None	OD-03/04	Design org assignment model	Team visibility/reassignment/denial audited/tested
CRM-08-T1	CRM	Web	Employee/manager	Targets	Define targets/metrics	P3	DEFERRED	Stable WORK/CRM	No domain found	None	Metric approval	Create dictionary before schema	Reproducible approved metrics and access tests
CRM-09-T1	CRM	Web	Manager	Reports	Build reconciled standard reports	P2	MISSING	Stable CRM	No complete report APIs	None	Metrics	Build after transaction truth	Reports reconcile and export/access/load tests pass
DOC-01	Backend/DB	API	Authorized	Files	Implement private object storage	P0	MISSING	OD-07	Client storage keys/placeholder s	None	Provider decision	Threat model/upload/download adapter	Type/size/access /expiry/retention/ audit tests pass
DOC-02	Backend/CRM/Customer	API/Web/Mobile	Customer/employee	PDF	Generate protected quotation PDF	P1	PLACEHOLDER	DOC-01, CRM-06	pdf_placeholder	None	DOC-01	Create immutable/versioned renderer	Amount/version match DB; signed access and snapshot tests pass
PAY-01	Backend/DB	API	Customer/finance	Payment	Decide pilot/manual vs gateway policy	P0	BLOCKED	OD-05	Reference + employee confirm flow	Unit foundation	Provider/business choice	Approve state/reconciliation model	Decision recorded with controls and migration plan
PAY-02	Backend/CRM/Customer	Full	Customer/finance	Payment	Implement approved confirmation/reconciliation	P1	PLACEHOLDER	PAY-01, DB-02	No gateway/webhook	None	PAY-01	Build signed/idempotent flow	Amount/order/signature/replay/refund/reconcile E2E passes
ERP-01-T1	ERP/Backend	Web/API	Employee/manager	Event Control	Prove booking → Event Record handoff	P1	IMPLEMENTED — UNVERIFIED	DB-01, PAY-01	Code/routes/tables exist	Unit only	Real DB	Add integration/E2E	One idempotent linked event, audit/outbox and denial proven
ERP-02-T1	ERP	Web	Manager	Manager Ops	Complete assignment/task/progress slice	P1	PARTIAL	WORK-01	Routes/APIs/tables exist	Unit only	Task model	Align with work model, add E2E	Manager assigns; employee executes; progress reconciles
V-01-T1	CVW Mobile	Vendor	Vendor	Home/Work	Prove assigned work vertical slice	P1	PARTIAL	DB-01, DOC-01	Dashboard/assignment/progress exists	Incomplete	Evidence storage	Test registry→assign→accept→complete	Strict own scope and ERP/mobile E2E pass
V-03-T1	Backend/DB/Mobile	Vendor	Vendor/employee	Catalogue	Design application/KYC/Listing/pricing approval	P2	MISSING	DOC-01, approvals	Foundation vendor/category only	None	Marketplace policy	Schema/API/state ADR	Base price hidden; version/review/publication E2E passes
V-04-T1	CVW/ERP	Vendor/Finance	Vendor/finance	Earnings	Complete invoice/settlement self-service	P2	PARTIAL	DOC-01, ERP-07	Settlement foundation	Unit only	Finance policy	Reconcile event/vendor amounts	Own-data, approval, payment and dispute tests pass
W-01-T1	CVW Mobile	Worker	Worker	Tasks	Prove task/attendance vertical slice	P1	PARTIAL	DB-01, DOC-01	Task detail/attendance foundation	Incomplete	Privacy/evidence	Test assign→respond→work→complete	Scope, timestamps, proof and ERP/mobile E2E pass
W-05-T1	Backend/DB/Mobile	Worker	Worker/employee	Profile	Build application/approval/skills/availability	P2	PARTIAL	DOC-01, AUTH-03	Worker create/update/skills exist	Unit foundation	Identity/privacy policy	Design self-application lifecycle	Approved role issuance and privacy/file E2E pass
EM-00	Employee Mobile	Flutter	Employees	Foundation	Approve separate app ADR and shared-code boundary	P0	BLOCKED	OD-02/03/04	No app/surface; reusable screens stranded	None	Architecture approval	Decide package/surface/IDs/reuse	ADR accepted; no duplicate backend/data/business logic

ID	Application	Interface	Role	Module	Task	Pri	Status	Dependency	Evidence	Test status	Blocker	Next action	Definition of Done
EM-01-T1	Employee Mobile	Mobile	Sales Person	First slice	Build login → My Work → My Leads → Follow-up → Profile	P1	MISSING	EM-00, CRM-02/03, AUTH-01	No production shell	None	Dependencies	Create role-by-role vertical slice	Signed test builds + API/DB/device E2E + revocation pass
EM-02-T1	Employee Mobile	Mobile	Telecaller	Second slice	Add call queue/outcomes/overdue	P2	MISSING	EM-01, CRM-03	No explicit role/domain	None	Persona approval	Narrow capability bundle and UI	Scoped queue/outcome/next-action/E2E pass
EM-03-T1	Employee Mobile	Mobile	Manager	Third slice	Add team work/approvals/escalations	P2	MISSING	CRM-07, approvals	Manager APIs event-focused	None	Hierarchy/work model	Mobile-safe manager views	Team scope, decisions, audit and E2E pass
EM-04-T1	Employee Mobile	Mobile	Field/Event Manager	Fourth slice	Add today's events/tasks/issues/proofs	P2	MISSING	ERP-02, DOC-01, NOTIF-01	Reusable ops screens exist	None	EM foundation	Extract/rebuild against approved APIs	Field execution web/mobile consistency and E2E pass
ERP-05-T1	ERP	Web	Warehouse/ops	Inventory	Prove stock allocation/custody	P1	IMPLEMENTED — UNVERIFIED	DB-01	Extensive tables/APIs/routes	Unit only	Real DB	Add concurrency/reconcile E2E	No negative/lost stock; custody/audit proven
ERP-06-T1	ERP/DB	Web/API	Procurement	Procurement	Design requisition → PO → receipt	P2	MISSING	Inventory, approvals	Suppliers only	None	Business/accounting rules	Write PRD/ADR/schema	Segregation/reconciliation/DB/E2E pass
ERP-07-T1	ERP	Web/API	Finance	Finance	Approve accounting/reconciliation controls	P1	PARTIAL/HIGH RISK	PAY-01, DB-01	Broad APIs/tables/routes	Unit only	Finance policy	Threat/model and reconciliation tests	Totals, approvals, refunds, settlements and audit reconcile
ERP-08-T1	ERP/DB	Web/API	Approvers	Approvals	Build unified controlled approval inbox	P2	MISSING/PARTIAL	AUTH-03, DOC-01	Some capability/actions	None	Approval catalogue	Define types/separation	No unauthorized/self/double approval; full audit
ERP-09-T1	ERP	Web	Admin/auditor	Administration	Build safe user/role/policy/audit product	P2	PARTIAL	AUTH-03	Backend foundations only	Incomplete	High-risk control design	Start with read/audit, then controlled writes	Least privilege, recovery and browser security tests pass
ERP-10-T1	ERP	Web	Manager/auditor	Reports	Build operational/financial reports	P2	MISSING/PARTIAL	Stable source modules	Summary APIs only	None	Metric dictionary	Reconcile one report at a time	Source totals/access/export/performance pass
NOTIF-01	Backend/DB	API	All	Notifications	Implement reliable delivery foundation	P1	PLACEHOLDER	Provider decision, DB-01	Outbox topics; pushIntegrated: false	Narrow processors only	Provider/inbox model	Provider adapter, tokens, inbox, retry/DLQ	Delivery/dedupe/privacy/deep-link/monitoring tests pass
NOTIF-02	Backend/Employee	API/UI	Employee/manager	Escalations	Implement due/overdue escalation rules	P2	MISSING	WORK-01, NOTIF-01	No generic work escalation	None	SLA/business policy	Start with lead first response	Employee → manager escalation is timed, deduped and audited
SOC-01	CRM/Backend	Web/API	Marketing/sales	Lead channels	Decide social integrations and consent	P2	BLOCKED	OD-09	Lead sources include campaign; no providers	None	Provider/consent	Select channels and data contract	Authorized, consented, deduped lead ingestion E2E passes
REL-01	DevOps	Backend/Web	Operators	Staging	Provision staging, secrets, HTTPS and monitoring	P0	MISSING	OD-10	Hosting undecided	None	Platform/owner	Approve and implement staging	Health/log/alert/deploy/rollback smoke passes
REL-02	DevOps	Database	Operators	Recovery	Automate backups and perform restore drill	P0	MISSING	REL-01	Docs only	No drill	Provider	Configure and time restore	Restore to clean environment meets approved RPO/RTO

ID	Application	Interface	Role	Module	Task	Pri	Status	Dependency	Evidence	Test status	Blocker	Next action	Definition of Done
REL-03	CVW Mobile	Android/iOS	Public roles	Store	Production-sign and beta-test CVW app	P0	BROKEN/MISSING	STAB/AUTH/REL	Debug signing; no iOS proof	Debug only	Accounts/IDs	Configure AAB/IPA/TestFlight/internal	Signed artifacts, privacy review and pilot E2E pass
REL-04	Employee Mobile	Android/iOS	Employees	Store	Production-sign and beta-test Employee app	P1	MISSING	EM-01, AUTH/REL	No app	None	EM dependencies	Store setup with controlled access	Signed AAB/IPA, revocation and pilot E2E pass
REL-05	DevOps	All	Operators	Production	Controlled Hyderabad rollout	P0	MISSING	All pilot P0/P1 gates	No live host/CD	None	Release readiness	Run go/no-go checklist	Monitored staged launch, rollback/support/incident ownership live

26. Recommended Build Order

Do not build every screen first. Complete one connected vertical slice, prove it, then expand.

Phase	Modules	What / Why / Where / Test / Done
0 — Stabilize	STAB-01-04, CI-01	Make current work trustworthy. Fix gates, classify changes, quarantine raw exports, replace broken assets. Done when local and CI static/unit/widget gates are green.
1 — Prove database/integration	DB-01-03, CI-02, C-03-T2	Run all migrations against clean Postgres and automate enquiry→lead. Done when retry, rollback, audit and outbox are proven in CI.
2 — Secure identity/access	AUTH-01-04	Production OTP, least privilege, distributed abuse decision and backend-only mobile data. Done when staging auth/revocation/denial tests pass.
3 — Customer core	C-01-05	Final navigation and live Home/Explore/Enquire/Plan/Profile. Done when one customer journey works on Android/iOS test devices.
4 — CRM core	CRM-01, WORK-01, CRM-02-05	Ownership, My Work, follow-up, Customer 360 and pipeline. Done when an enquiry is handled within SLA with traceable activity/outcome.
5 — Document/payment/booki ng	CRM-06, DOC-01/02, PAY-01/02, ERP-01	Protected quote, approval, payment and idempotent booking/Event Record. Done when money/document controls and E2E reconcile.
6 — Event/manager operations	ERP-01/02	Stable Event Record, manager tasks/progress. Done when manager assignment to completion is audited and tested.
7 — Vendor	V-01-05, ERP-03	Complete application, catalogue/pricing, work order, evidence and settlement one slice at a time.
8 — Worker	W-01-05, ERP-04	Complete application, tasks, attendance, evidence, earnings and profile one slice at a time.
9 — Employee Mobile	EM-00, EM-01-04	Create separate app after work/role APIs stabilize: Sales Person first, then Telecaller, Manager, Field/Event. Never copy ERP.
10 — Inventory/procurement	ERP-05/06	Prove inventory custody/concurrency, then build procurement with segregation/reconciliation.
11 — Finance	ERP-07	Reconcile payment, expenses, settlements, invoices/receipts under approved policy.
12 — Admin/reporting	CRM-07-10, ERP-08-10	Hierarchy, approvals, administration, metric dictionary and reconciled reports.
13 — Notifications/integrations	NOTIF-01/02, SOC-01	Reliable inbox/push/escalation and approved lead channels after source workflows are authoritative.
14 — Release hardening	REL-01-05	Staging, monitoring, restore, signed store releases, privacy/security/performance and controlled Hyderabad launch.

Why Employee Mobile is Phase 9 but starts planning earlier

Create its ADR, capability matrix and app identity during Phases 2–4. Build its production screens only after My Work/follow-up/task APIs are stable. This prevents a second mobile UI from forcing duplicate data and rework. A Sales Person vertical slice can begin before every ERP module is complete because it depends mainly on identity, leads, follow-up and notifications.

27. Daily Development Process

Use this ten-step loop for every module.

1. **Understand — WHAT/WHY:** explain the user, business result and data in simple language.
2. **Inspect — WHERE:** find current screens, API, tables, capabilities, tests and docs.
3. **Gap analysis:** label each part Done, Unverified, Partial, Placeholder, Broken, Blocked, Missing or Deferred.
4. **Plan — HOW:** select the smallest complete UI → API → DB → authorization slice; name files and exit gate.
5. **Protect:** create a small branch/change group; do not mix cleanup with a feature.
6. **Implement:** reuse contracts/design patterns; no direct DB from clients; no invented statuses/permissions.
7. **Focused test — TEST:** unit/widget/repository/API tests for happy, denial, invalid-state, retry and stale-version paths.
8. **Integrate:** run against migrated PostgreSQL and the real interface.
9. **Verify — DONE:** run complete gates, inspect audit/outbox/data and capture evidence.
10. **Update roadmap:** change status/evidence, record remaining risk and set exactly one next task.

Daily rule for a non-technical founder

Ask Codex for only this:

“Work on roadmap item **<ID>** only. First tell me WHAT, WHY, WHERE, HOW, TEST and DONE. Inspect current code, implement the smallest complete slice, run the exit gate, and update the roadmap. Do not start the next module.”

28. Current Module

STAB-01 — Repository Quality Gate Restoration

What: Make the existing project's checks green without adding a new feature.

Why: New work on a red, mixed repository hides regressions and makes every later decision less trustworthy.

Where: Root formatting/lint configuration and owned source/docs; `apps/mobile/test/home_tab_test.dart` plus its Home implementation; `.github/workflows/ci.yml`; design/raw export boundaries.

How:

1. Preserve/classify current changes.
2. Exclude/archive raw Stitch debug exports from source formatting or normalize only files that are intended source.
3. Fix the one Next image lint issue correctly.
4. Resolve the 20 Home tests by comparing intended current UI behavior, not by blindly deleting assertions.
5. Correct CI branch/API-port drift after branch decision.
6. Run complete root and Flutter gates.

Test: root format, lint, typecheck, unit tests, build; Flutter format/analyze/test; CI-equivalent commands.

Done: all existing gates pass with no skipped failing tests and no unrelated feature change.

29. Exact Next Task

STAB-01A — Create a safe formatter/asset boundary and restore the TypeScript static gate

Immediate action: classify the 280 formatter findings into owned source/docs versus raw/generated exports; configure the formatter to ignore only proven raw/generated material; format/fix owned files; replace the single raw `<img>` usage with the project-approved Next image approach (or record an explicit justified exception); then run format, lint, typecheck, tests and build.

Why this is first: it is small, reversible and removes noise before debugging Flutter Home behavior or changing architecture. It also prevents gzipped/raw Stitch exports from repeatedly breaking source checks.

Do not do in this task: no new app, no Employee Mobile scaffold, no table migration, no production provider, no bulk delete and no navigation rewrite.

Exit Gate

The task is complete only when:

1. root format check passes;
2. root lint passes with zero warnings;
3. root typecheck, tests and build still pass;
4. ignore rules name only proven generated/raw paths;
5. no product source/evidence is deleted;
6. the change list contains only static-gate restoration;
7. the roadmap evidence for STAB-01 is updated.

After STAB-01A, do **STAB-01B: resolve the 20 Flutter Home tests**, then complete CI alignment.

30. Definition of Done

Module-level Definition of Done

A module is Done only if all applicable boxes are true:

- ☐ Business purpose, user and approved states are documented.
- ☐ UI covers loading, empty, populated, validation, error, offline/retry and accessibility states.
- ☐ Versioned API contract is shared and validated.
- ☐ Database migration is ordered, reviewed and tested on a clean database.
- ☐ Authentication, capability, branch/team/assignment/record scope and state/version checks are server-enforced.
- ☐ Critical create/update commands are idempotent and concurrency-safe.
- ☐ Audit/activity/outbox semantics are correct and not duplicated.
- ☐ Sensitive fields/files are minimized, masked and protected.
- ☐ Unit, widget/component, database, API and one end-to-end journey pass.
- ☐ Logs/metrics/errors are useful without leaking secrets or personal data.
- ☐ Documentation, Master TODO status, evidence and exact next task are updated.

Hyderabad pilot Definition of Done

- Customer can authenticate, browse approved content, enquire, receive/act on a protected quote and complete the approved payment path.
- CRM can own, follow up and convert the same enquiry without copying records.
- ERP receives one booking/Event Record and can assign manager/vendor/worker, execute minimal operations and reconcile finance.
- Vendor/Worker can securely act only on assigned work.
- Production OTP, HTTPS, secrets, private documents, audit, monitoring, support and rollback are operating.
- Clean database migrations, API integration, browser/device E2E, security checks and backup restore evidence are green.
- Signed CVW AAB/IPA pass internal/TestFlight pilot; Employee Mobile release is required only if its approved pilot role is in launch scope.

Production Definition of Done

Pilot gates plus complete role products, notification delivery, payment/file integrations, procurement/finance/admin/reporting scope selected for launch, capacity/performance proof, incident/on-call ownership, privacy/store declarations, staged releases and successful restore/rollback drills.

31. Open Decisions / Risks

Significant conflicts are not silently changed. Record approval in an ADR or product decision before implementation.

OPEN DECISION OD-01 — Customer navigation

- **Existing:** Home → Explore → Plan → Enquiries → Account.
- **Intended:** Home → Explore → Enquire → Plan → Profile.
- **Conflict:** Existing enum/order/routes/tests and saved/deep links use the old structure.
- **Recommendation:** accept the intended structure; make Enquire contain creation plus enquiry/quote/booking history; rename Account to Profile; migrate links/tests intentionally.
- **Impact:** focused Flutter navigation/state/test change; no backend/database duplication.

OPEN DECISION OD-02 — Employee Mobile application boundary

- **Existing:** employee roles resolve only to employee web; some manager/ops Flutter screens are stranded inside `apps/mobile`.
- **Intended:** separate production Employee Mobile app for Android/iOS.
- **Recommendation:** create `apps/employee-mobile` as a separate Flutter package after an ADR; add `employee_mobile` bootstrap surface; extract only proven reusable design/API packages, not business records or backend logic.
- **Impact:** new store identities, signing, CI jobs, push credentials and role-based release plan; same identity/backend/database.

OPEN DECISION OD-03 — Employee personas, roles and hierarchy

- **Existing:** `employee`, `support`, `finance`, `manager`, `administrator`, `auditor`; broad `employee` capabilities; no department/team hierarchy.
- **Intended:** Sales Person, Telecaller, Marketing, Sales Manager, General Manager and Field/Event personas.
- **Recommendation:** capabilities + scoped assignments first; add explicit business roles only where stable policy needs them; build hierarchy/team model before team visibility.
- **Impact:** security migration and denial-test program; avoids UI-only roles.

OPEN DECISION OD-04 — Common employee work model

- **Existing:** lead activities, event tasks and operations tasks are separate domain mechanisms.
- **Intended:** one traceable assignment/activity/outcome/next-action/escalation experience.
- **Recommendation:** ADR comparing generalization versus orchestration/projection. Preserve domain ownership; add a generic work record only if it eliminates duplication.
- **Impact:** foundational dependency for My Work, follow-up, Employee Mobile, manager monitoring and notifications.

OPEN DECISION OD-05 — Payment model/provider

- **Existing:** customer submits method/reference; employee confirms; no gateway/webhook/reconciliation.

- **Recommendation:** explicitly approve controlled manual Hyderabad pilot controls or select gateway; define states, signature/replay, amount match, refunds, reconciliation and incident handling.
- **Impact:** booking integrity, finance and production claim.

OPEN DECISION OD-06 — Production OTP/SMS provider

- **Existing:** local OTP only; external provider returns 503.
- **Recommendation:** select compliant provider, failover/support owner and shared abuse controls.
- **Impact:** all production authentication and store pilots.

OPEN DECISION OD-07 — Private file/object storage

- **Existing:** placeholders/client-supplied storage keys.
- **Recommendation:** select private object storage; NestJS authorizes server-created upload/download intents; define validation, retention, encryption, malware handling and signed expiry.
- **Impact:** quotation PDF, KYC, proof, invoices and privacy.

OPEN DECISION OD-08 — Employee Mobile scope

- **Existing:** all employee roles are web-only.
- **Recommendation:** launch role-by-role: Sales Person first, then Telecaller, Manager, Field/Event; keep bulk/admin/complex finance on web.
- **Impact:** controls initial app size and avoids miniature ERP.

OPEN DECISION OD-09 — Social lead integrations

- **Existing:** lead source supports `campaign`; no social providers/consent pipeline.
- **Recommendation:** identify actual channels (for example ads/messaging), provider APIs, consent, opt-out, retention, deduplication and ownership before integration.
- **Impact:** CRM marketing scope, privacy and recurring provider cost.

OPEN DECISION OD-10 — Hosting, monitoring and recovery owner

- **Existing:** no live host/CD/cloud inventory; Docker Compose is local only.
- **Recommendation:** choose managed PostgreSQL, Nest process host, Next host, object storage/queue/monitoring and named operator; require separate staging/production and restore drill.
- **Impact:** every production release.

OPEN DECISION OD-11 — Git default branch

- **Existing:** repository active branch `master`; CI push trigger `main`.
- **Recommendation:** select one canonical protected default branch and update CI/docs/rules together.
- **Impact:** pushes may currently skip CI.

OPEN DECISION OD-12 — Supabase usage boundary

- **Existing:** Supabase Flutter initialization/direct read conflicts with accepted backend-only boundary; managed Supabase PostgreSQL hosting is allowed.
- **Recommendation:** remove client DB dependency and bundled client environment after usage trace; keep Supabase only as a PostgreSQL/object-storage provider if selected behind NestJS.
- **Impact:** security, architecture and mobile configuration.

Risk register

Risk	Likelihood / impact	Control
Adding features before green gates	High / High	Finish Phase 0 and enforce CI
Accidental deletion in dirty tree	High / High	Cleanup manifest, review, backup, rebuild; no bulk delete
Broad employee data exposure	Medium / Critical	OD-03, server scope, denial tests and field filtering
Duplicate task/work systems	High / High	OD-04 ADR before schema/UI
Payment/file/OTP placeholders mistaken for live	High / Critical	Honest labels and release-blocking provider E2E
Store rejection or signing loss	Medium / High	Organization accounts, secure custody, early TestFlight/internal track
Database migration defect	Medium / Critical	Clean integration CI, backups and restore drill
Sample metrics/data used for decisions	High / High	Label/remove samples; reports must reconcile to source
Notification loss/duplicates	High / Medium	Transactional outbox, idempotent consumer, retry/DLQ/monitoring
Documentation drift	High / Medium	Update roadmap/evidence at every exit gate

Final roadmap logic

CURRENT STATE
↓
STABILIZE
↓
PROVE DATABASE
↓
SECURE IDENTITY
↓
CUSTOMER
↓
CRM + EMPLOYEE WORK
↓
QUOTATION / DOCUMENT / PAYMENT
↓
EVENT RECORD / ERP
↓
VENDOR
↓
WORKER
↓
EMPLOYEE MOBILE — ROLE BY ROLE
↓
INVENTORY / PROCUREMENT
↓
FINANCE
↓
ADMIN / REPORTING
↓
NOTIFICATIONS / INTEGRATIONS
↓
TESTING / SECURITY / RECOVERY
↓
GOOGLE PLAY / APP STORE / PRODUCTION RELEASE

One project. Two mobile store applications. One employee web portal. One NestJS backend. One PostgreSQL source of truth. Build and prove one connected module at a time.
